

Form detail

#86: Weekly Report #12 July 6 - July 12, 2026



Forms

Location	
Form date	Jul 6, 2026
Template	Project Status Report
Description	Week of July 6 - July 12, 2026
Due date	Jul 28, 2026
Submitted by	Jordan Gent
Submitter's company	CCR Construction Ltd
Status	Closed
Last update	Jul 28, 2026, 1:57 PM CST
Last updated by	Jordan Gent
Included references	Assets Files Forms Issues Photos File Packages Sheets Submittals RFIs PCOs Schedule Activities

1. Monday

- 1.1 Date
July 6, 2026
- 1.2 Work Completed
Framing walls for new addition, removing shoring from inside new reservoir, site clean up and pumping water, cut existing roof for lift preparation.

Photos (7)[IMG_4940.jpeg](#)

Added as Reference

Taken on Jul 6, 2026, 3:15 PM CST

Added on Jul 6, 2026, 6:38 PM CST

Added by Jeff Anderson

[IMG_4947.jpeg](#)

Added as Reference

Taken on Jul 6, 2026, 3:18 PM CST

Added on Jul 6, 2026, 6:37 PM CST

Added by Jeff Anderson

[IMG_4946.jpeg](#)

Added as Reference

Taken on Jul 6, 2026, 3:18 PM CST

Added on Jul 6, 2026, 6:37 PM CST

Added by Jeff Anderson

[IMG_4948.jpeg](#)

Added as Reference

Taken on Jul 6, 2026, 4:10 PM CST

Added on Jul 6, 2026, 6:37 PM CST

Added by Jeff Anderson



[IMG_4942.jpeg](#)

Added as Reference

Taken on Jul 6, 2026, 3:15 PM CST

Added on Jul 6, 2026, 6:38 PM CST

Added by Jeff Anderson




[IMG_4936.jpeg](#)

Added as Reference

Taken on Jul 6, 2026, 8:55 AM CST

Added on Jul 6, 2026, 6:38 PM CST

Added by Jeff Anderson

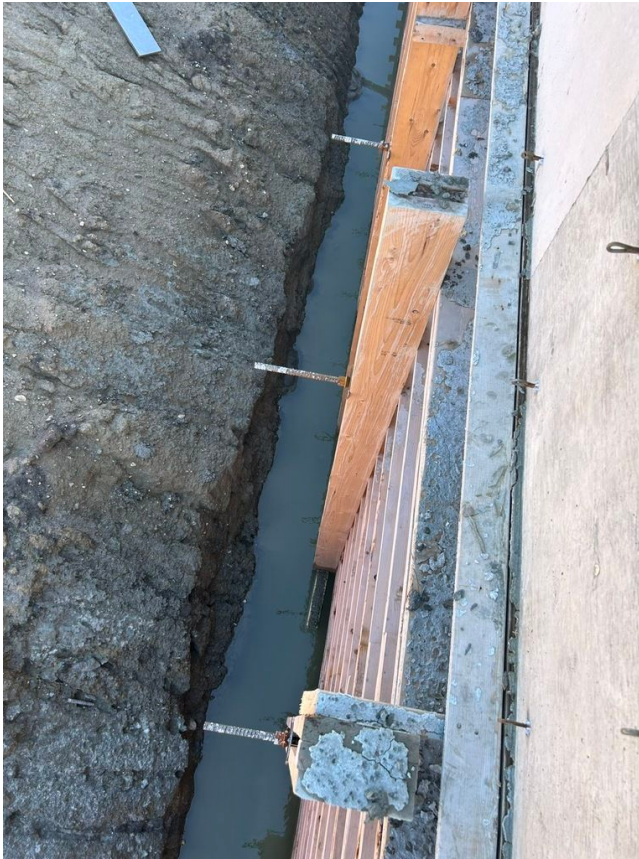

[IMG_4935.jpeg](#)

Added as Reference

Taken on Jul 6, 2026, 8:54 AM CST

Added on Jul 6, 2026, 6:38 PM CST

Added by Jeff Anderson

2. Tuesday

2.1 Date

July 7, 2026

2.2 Work Completed

Demolition of existing building mechanical and electrical fixed to walls and ceiling, removing forms inside existing reservoir and exterior, framing of new building walls and roof sections.

Photos (4)[IMG_4961.jpeg](#)**Added as Reference****Taken on** Jul 7, 2026, 4:11 PM CST**Added on** Jul 7, 2026, 7:30 PM CST**Added by** Jeff Anderson[IMG_4962.jpeg](#)**Added as Reference****Taken on** Jul 7, 2026, 4:13 PM CST**Added on** Jul 7, 2026, 7:30 PM CST**Added by** Jeff Anderson[IMG_4958.jpeg](#)**Added as Reference****Taken on** Jul 7, 2026, 4:10 PM CST**Added on** Jul 7, 2026, 7:32 PM CST**Added by** Jeff Anderson[IMG_4952.jpeg](#)**Added as Reference****Taken on** Jul 7, 2026, 4:07 PM CST**Added on** Jul 7, 2026, 7:32 PM CST**Added by** Jeff Anderson**3. Wednesday**

3.1 Date
July 8, 2026

3.2 Work Completed

Craning in and installing new walls and roof for new building addition, supporting existing mechanical and electrical inside of existing building, stripping forms from exterior of reservoir.

Photos (8)[IMG_5004.jpeg](#)**Added as Reference****Taken on Jul 8, 2026, 3:23 PM CST****Added on Jul 8, 2026, 6:26 PM CST****Added by Jeff Anderson**[IMG_5006.jpeg](#)**Added as Reference****Taken on Jul 8, 2026, 3:24 PM CST****Added on Jul 8, 2026, 6:26 PM CST****Added by Jeff Anderson**[IMG_4997.jpeg](#)**Added as Reference****Taken on Jul 8, 2026, 3:21 PM CST****Added on Jul 8, 2026, 6:27 PM CST****Added by Jeff Anderson**[IMG_5003.jpeg](#)**Added as Reference****Taken on Jul 8, 2026, 3:23 PM CST****Added on Jul 8, 2026, 6:26 PM CST****Added by Jeff Anderson**

[IMG_4998.jpeg](#)

Added as Reference

Taken on Jul 8, 2026, 3:22 PM CST

Added on Jul 8, 2026, 6:27 PM CST

Added by Jeff Anderson

[IMG_4995.jpeg](#)

Added as Reference

Taken on Jul 8, 2026, 3:20 PM CST

Added on Jul 8, 2026, 6:27 PM CST

Added by Jeff Anderson

[IMG_4990.jpeg](#)

Added as Reference

Taken on Jul 8, 2026, 2:42 PM CST

Added on Jul 8, 2026, 6:27 PM CST

Added by Jeff Anderson

[IMG_4974.jpeg](#)

Added as Reference

Taken on Jul 8, 2026, 12:28 PM CST


Added on Jul 8, 2026, 6:28 PM CST

Added by Jeff Anderson

4. Thursday

4.1 Date
July 9, 2026

4.2 Work Completed
Straighten walls and install blocking, clean up site and forms to be removed from site, general clean up.

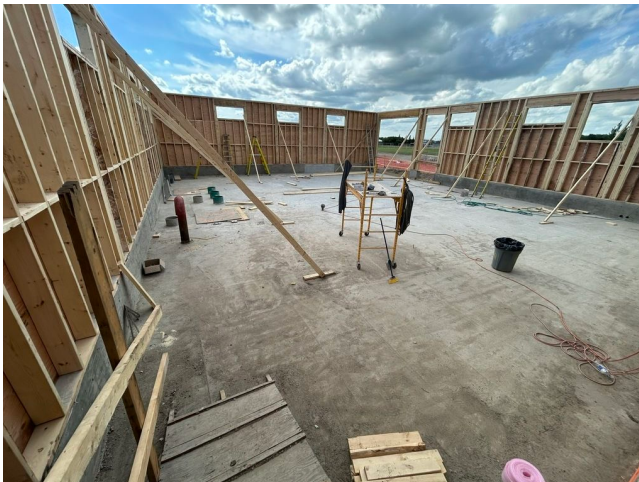Photos (3)[IMG_5028.jpeg](#)**Added as Reference****Taken on** Jul 9, 2026, 4:33 PM CST**Added on** Jul 9, 2026, 8:27 PM CST**Added by** Jeff Anderson[IMG_5027.jpeg](#)**Added as Reference****Taken on** Jul 9, 2026, 4:33 PM CST**Added on** Jul 9, 2026, 8:27 PM CST**Added by** Jeff Anderson[IMG_5032.jpeg](#)**Added as Reference****Taken on** Jul 9, 2026, 4:33 PM CST**Added on** Jul 9, 2026, 8:27 PM CST**Added by** Jeff Anderson**5. Friday**

5.1 Date
July 10, 2026

5.2 Work Completed
N/A

6. Saturday/Sunday

6.1 Date
July 11/12, 2026

6.2 Work Completed
N/A

Notes

Next Week Look Ahead:

Install curb in the existing building

Finish installing supports for mechanical in existing building

Patch holes in reservoir in new reservoir

Install truss blocking, hangers and roof sheathing

Finish installing remaining roof trusses
