

Form detail

#114: Weekly Report #19 - August 24 - 30, 2026



Forms

Location

Form date Aug 31, 2026

Template Project Status Report

Description Redvers WTP Upgrade - Weekly Report #19

Due date Aug 31, 2026

Submitted by Jordan Gent

Submitter's company CCR Construction Ltd

Status Closed

Last update Aug 31, 2026, 3:30 PM CST

Last updated by Jordan Gent

Included references Assets | Files | Forms | Issues | Photos | File Packages | Sheets | Submittals | RFIs | PCOs | Schedule Activities

1. Monday

1.1 Date
August 24, 2026

1.2 Work Completed
Install base flashing and wood blocking for masonry, framing mechanical openings in exterior walls, backfill and level perimeter of site, install pipe in waste pit and placing floor drains, setting up scaffolding and started installing building wrap.

Photos (4)

[IMG_5612.jpeg](#)

Added as Reference

Taken on Aug 24, 2026, 5:24 PM CST

Added on Aug 24, 2026, 6:56 PM CST

Added by Jeff Anderson

[IMG_5602.jpeg](#)

Added as Reference

Taken on Aug 24, 2026, 2:01 PM CST

Added on Aug 24, 2026, 6:56 PM CST

Added by Jeff Anderson

[IMG_5611.jpeg](#)

Added as Reference

Taken on Aug 24, 2026, 5:24 PM CST

Added on Aug 24, 2026, 6:56 PM CST

Added by Jeff Anderson

[IMG_5609.jpeg](#)

Added as Reference

Taken on Aug 24, 2026, 5:24 PM CST

Added on Aug 24, 2026, 6:56 PM CST

Added by Jeff Anderson

2. Tuesday

2.1 Date
August 25, 2026

2.2 Work Completed

Frame mechanical openings in exterior walls, finish base flashing for masonry, install piping in waste pit and reservoir, install masonry, spray foam exterior walls

Photos (6)



[IMG_5622.jpeg](#)

Added as Reference

Taken on Aug 25, 2026, 11:10 AM CST

Added on Aug 25, 2026, 9:00 PM CST

Added by Jeff Anderson



[IMG_5645.jpeg](#)

Added as Reference

Taken on Aug 25, 2026, 5:57 PM CST

Added on Aug 25, 2026, 9:00 PM CST

Added by Jeff Anderson



[IMG_5642.jpeg](#)

Added as Reference

Taken on Aug 25, 2026, 5:50 PM CST

Added on Aug 25, 2026, 9:00 PM CST

Added by Jeff Anderson



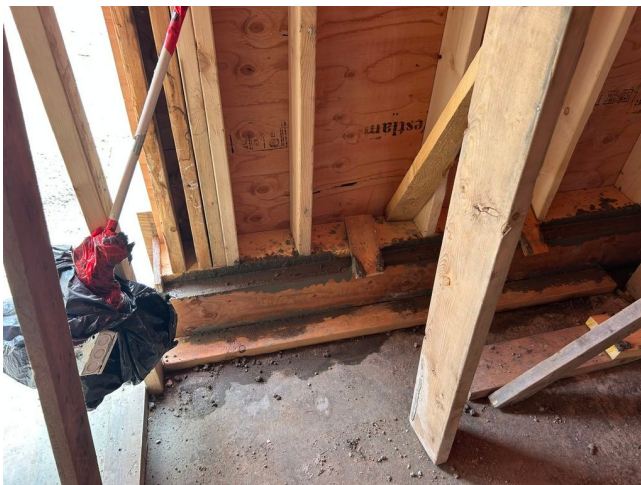
[IMG_5646.jpeg](#)

Added as Reference

Taken on Aug 25, 2026, 5:57 PM CST

Added on Aug 25, 2026, 9:00 PM CST

Added by Jeff Anderson

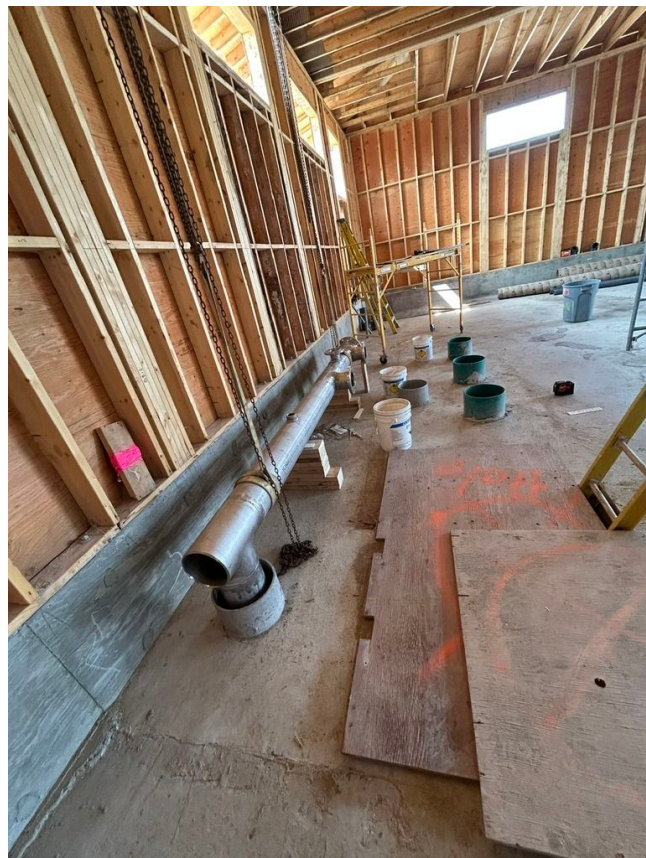
[IMG_5632.jpeg](#)

Added as Reference

Taken on Aug 25, 2026, 11:13 AM CST

Added on Aug 25, 2026, 9:00 PM CST

Added by Jeff Anderson

[IMG_5635.jpeg](#)

Added as Reference

Taken on Aug 25, 2026, 12:16 PM CST

Added on Aug 25, 2026, 9:00 PM CST

Added by Jeff Anderson

3. Wednesday

3.1 Date

August 26, 2026

3.2 Work Completed

Cleaning out reservoir, spray foam exterior walls, installing masonry, installing piping in reservoir and venting at the washroom

Photos (5)

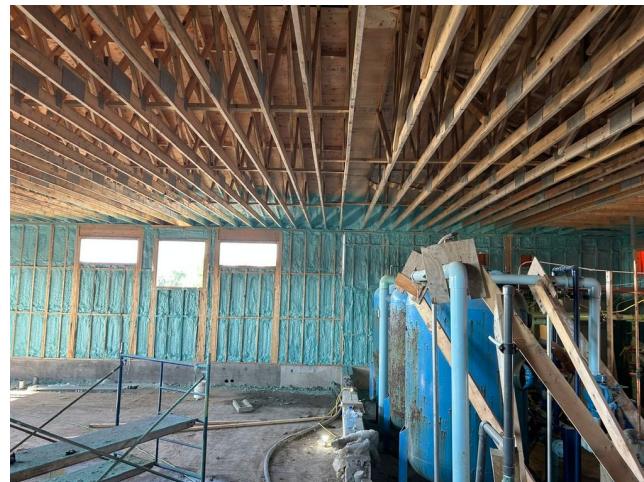
[IMG_5662.jpeg](#)

Added as Reference

Taken on Aug 26, 2026, 5:31 PM CST

Added on Aug 26, 2026, 7:26 PM CST

Added by Jeff Anderson

[IMG_5659.jpeg](#)

Added as Reference

Taken on Aug 26, 2026, 5:31 PM CST

Added on Aug 26, 2026, 7:26 PM CST

Added by Jeff Anderson

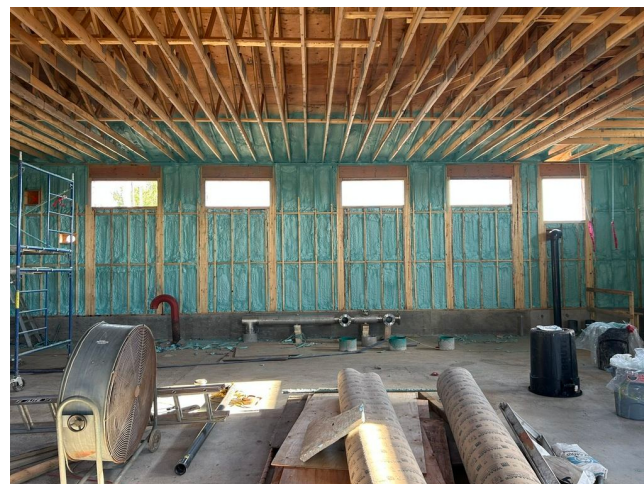
[IMG_5663.jpeg](#)

Added as Reference

Taken on Aug 26, 2026, 5:42 PM CST

Added on Aug 26, 2026, 7:26 PM CST

Added by Jeff Anderson

[IMG_5661.jpeg](#)

Added as Reference

Taken on Aug 26, 2026, 5:31 PM CST

Added on Aug 26, 2026, 7:26 PM CST

Added by Jeff Anderson



[IMG_5660.jpeg](#)

Added as Reference

Taken on Aug 26, 2026, 5:31 PM CST

Added on Aug 26, 2026, 7:26 PM CST

Added by Jeff Anderson

4. Thursday

4.1 Date
August 27, 2026

4.2 Work Completed
Install brick angle and masonry, install fascia board clean out reservoir and around site

Photos (4)



[IMG_5664.jpeg](#)

Added as Reference

Taken on Aug 26, 2026, 5:42 PM CST

Added on Aug 27, 2026, 8:55 PM CST

Added by Jeff Anderson



[IMG_5669.jpeg](#)

Added as Reference

Taken on Aug 27, 2026, 3:31 PM CST

Added on Aug 27, 2026, 8:55 PM CST

Added by Jeff Anderson



[IMG_5670.jpeg](#)
Added as Reference
Taken on Aug 27, 2026, 3:34 PM CST
Added on Aug 27, 2026, 8:55 PM CST
Added by Jeff Anderson



[IMG_5668.jpeg](#)
Added as Reference
Taken on Aug 27, 2026, 3:31 PM CST
Added on Aug 27, 2026, 8:55 PM CST
Added by Jeff Anderson

5. Friday

- 5.1 Date
 August 28, 2026
- 5.2 Work Completed
 N/A

6. Saturday/Sunday

- 6.1 Date
 August 29-30, 2026
- 6.2 Work Completed
 N/A

Notes

- Week Look Ahead:
- Install ceiling plywood
 - Install plywood on interior side of walls
 - Install framing for soffits
 - Form access hatches for reservoir
 - Prep for beam hoist install
 - Clean up of site
