

Form detail

#127: Weekly Report #20 - August 31 - September 6, 2026

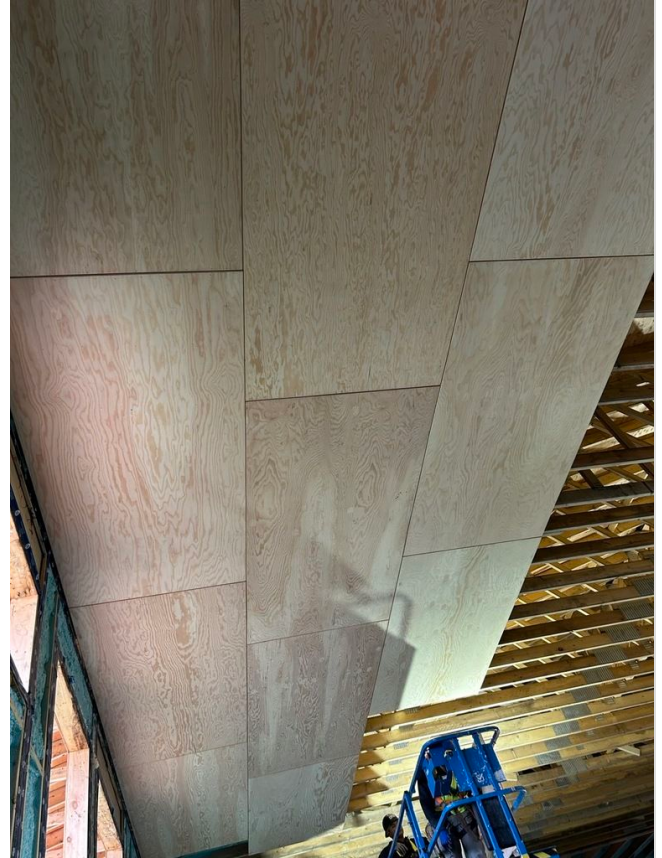


Forms

Location	
Form date	Sep 8, 2026
Template	Project Status Report
Description	Redvers WTP Upgrade - Weekly Report #20
Due date	Sep 11, 2026
Submitted by	Jordan Gent
Submitter's company	CCR Construction Ltd
Status	Closed
Last update	Sep 11, 2026, 3:55 PM CST
Last updated by	Jordan Gent
Included references	Assets Files Forms Issues Photos File Packages Sheets Submittals RFIs PCOs Schedule Activities

1. Monday

- 1.1 Date
August 31, 2026
- 1.2 Work Completed
Installing interior plywood on ceiling, finished installing fascia and started framing the soffit.

Photos (2)[IMG_5688.jpeg](#)**Added as** Reference**Taken on** Aug 31, 2026, 8:10 PM CST**Added on** Aug 31, 2026, 8:10 PM CST**Added by** Jeff Anderson[IMG_5689.jpeg](#)**Added as** Reference**Taken on** Aug 31, 2026, 5:05 PM CST**Added on** Aug 31, 2026, 8:10 PM CST**Added by** Jeff Anderson**2. Tuesday**

2.1 Date

September 1, 2026

2.2 Work Completed

Installing plywood on the ceiling and installing the columns in the exterior walls to support the lifting beam.

Photos (2)[IMG_5705.jpeg](#)**Added as Reference****Taken on** Sep 1, 2026, 5:21 PM CST**Added on** Sep 1, 2026, 7:58 PM CST**Added by** Jeff Anderson[IMG_5704.jpeg](#)**Added as Reference****Taken on** Sep 1, 2026, 7:58 PM CST**Added on** Sep 1, 2026, 7:58 PM CST**Added by** Jeff Anderson**3. Wednesday**

- 3.1 Date
September 2, 2026
- 3.2 Work Completed
Install plywood on ceilings and walls

Photos (5)[IMG_5716.jpeg](#)**Added as Reference****Taken on Sep 2, 2026, 5:20 PM CST****Added on Sep 2, 2026, 7:57 PM CST****Added by Jeff Anderson**[IMG_5714.jpeg](#)**Added as Reference****Taken on Sep 2, 2026, 7:57 PM CST****Added on Sep 2, 2026, 7:57 PM CST****Added by Jeff Anderson**[IMG_5710.jpeg](#)**Added as Reference****Taken on Sep 2, 2026, 5:18 PM CST****Added on Sep 2, 2026, 7:57 PM CST****Added by Jeff Anderson**[IMG_5712.jpeg](#)**Added as Reference****Taken on Sep 2, 2026, 7:57 PM CST****Added on Sep 2, 2026, 7:57 PM CST****Added by Jeff Anderson**



[IMG_5711.jpeg](#)

Added as Reference

Taken on Sep 2, 2026, 5:19 PM CST

Added on Sep 2, 2026, 7:57 PM CST

Added by Jeff Anderson

4. Thursday

4.1 Date

September 3, 2026

4.2 Work Completed

Install plywood on ceiling and walls and install drywall in the attic for smoke separation.

Photos (2)[20260904_124507_photo.jpeg](#)**Added as Reference****Taken on** Sep 4, 2026, 12:45 PM CST**Added on** Sep 4, 2026, 12:51 PM CST**Added by** Jared videogain[20260904_124412_photo.jpeg](#)**Added as Reference****Taken on** Sep 4, 2026, 12:44 PM CST**Added on** Sep 4, 2026, 12:51 PM CST**Added by** Jared videogain**5. Friday**

5.1 Date

September 4, 2026

5.2 Work Completed

Install plywood on ceilings and stripping forms in the new reservoir.**6. Saturday/Sunday**

6.1 Date

September 5-6, 2026

6.2 Work Completed
N/A.

Notes

Week Look Ahead:

Finish installing plywood on ceilings

Spray foam the ceiling space

Paint the plywood ceiling in the water treatment plant

Framing the partition wall between the existing and new plant

Install piping in the new reservoir
