

Form detail

#142: Weekly Report #21 - September 7 - 13, 2026



Forms

Location	
Form date	Sep 14, 2026
Template	Project Status Report
Description	Redvers WTP Upgrade - Weekly Report #21
Due date	Oct 1, 2026
Submitted by	Jordan Gent
Submitter's company	CCR Construction Ltd
Status	Closed
Last update	Oct 1, 2026, 4:24 PM CST
Last updated by	Jordan Gent
Included references	Assets Files Forms Issues Photos File Packages Sheets Submittals RFIs PCOs Schedule Activities

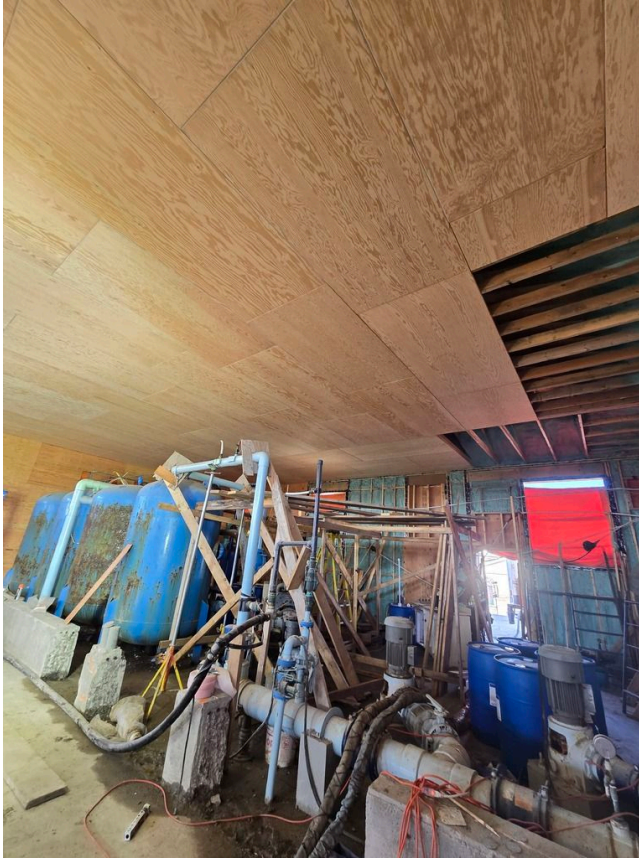
1. Monday

- 1.1 Date
September 7, 2026
- 1.2 Work Completed
Labour Day - N/A

2. Tuesday

- 2.1 Date

September 8, 2026**2.2 Work Completed**
Installed plywood on ceilings**Photos (1)**[20260908_181235_photo.jpeg](#)**Added as** Reference**Taken on** Sep 8, 2026, 6:12 PM CST**Added on** Sep 8, 2026, 6:16 PM CST**Added by** Jared videogain**3. Wednesday****3.1 Date**
September 9, 2026**3.2 Work Completed**
Installing plywood on ceilings, spray foam in ceiling

Photos (1)

[20260909_172111_photo.jpeg](#)

Added as Reference

Taken on Sep 9, 2026, 5:21 PM CST

Added on Sep 9, 2026, 5:22 PM CST

Added by Jared videogain

4. Thursday

4.1 Date

September 10, 2026

4.2 Work Completed

Install plywood on ceiling and framing of columns, primed ceiling, spray foam in roof trusses.

Photos (1)

[20260910_165449_photo.jpeg](#)

Added as Reference

Taken on Sep 10, 2026, 4:54 PM CST

Added on Sep 10, 2026, 4:56 PM CST

Added by Jared videogain

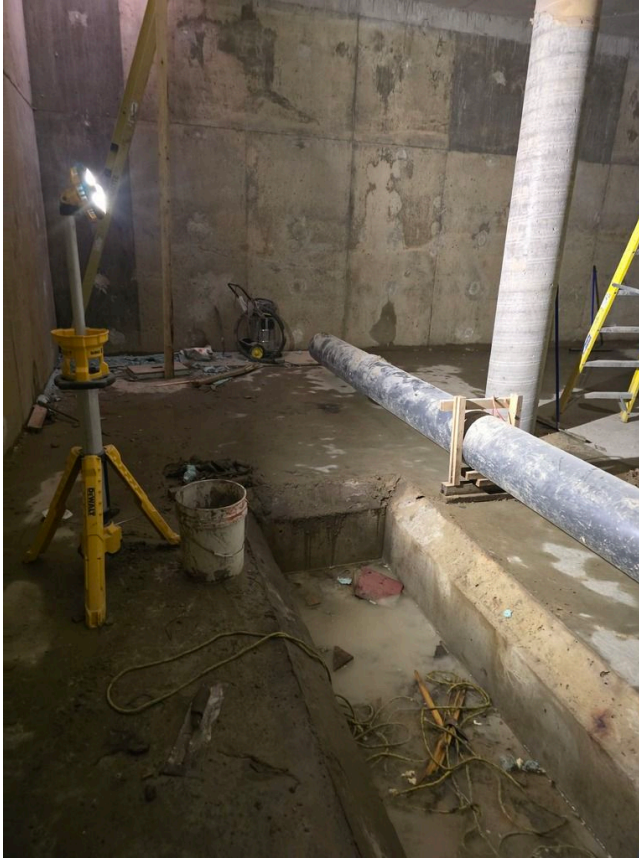
5. Friday

5.1 Date

September 11, 2026

5.2 Work Completed

Frame columns in wall for lifting beam install, layout grade beam, painting ceiling, spray foam in roof trusses, plumbing line installs in the reservoir.

Photos (6)

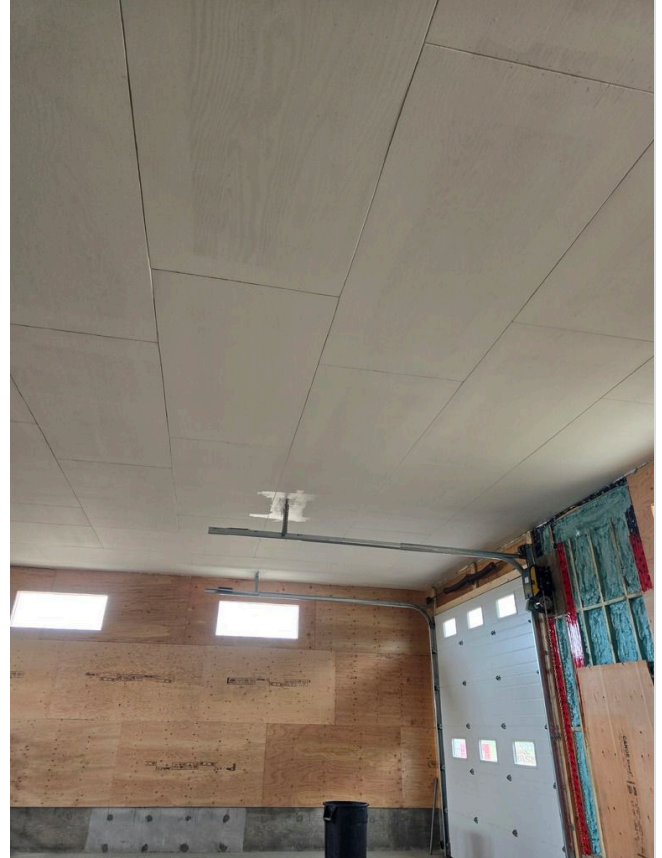
[20260911_110912_photo.jpeg](#)

Added as Reference

Taken on Sep 11, 2026, 11:09 AM CST

Added on Sep 11, 2026, 11:12 AM CST

Added by Jared videogain



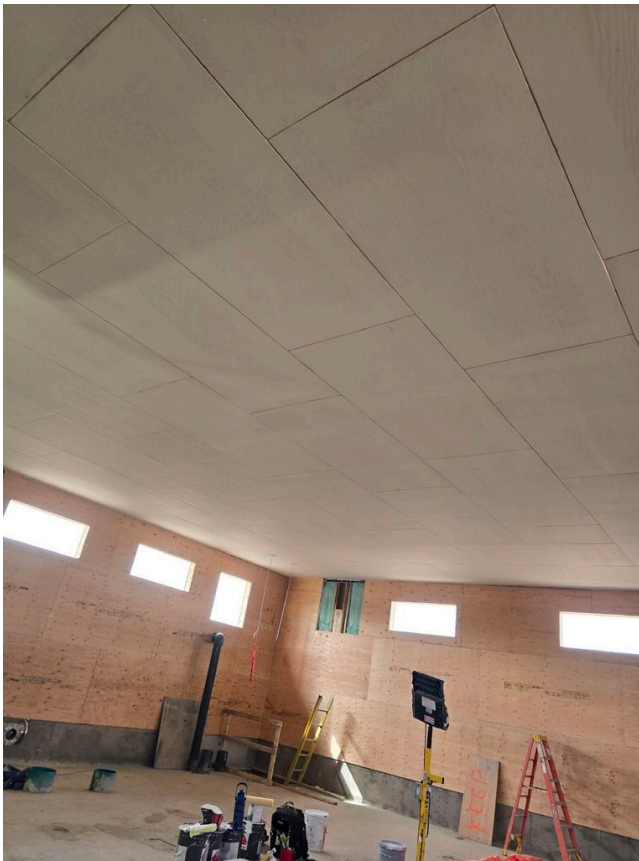
[20260911_110814_photo.jpeg](#)

Added as Reference

Taken on Sep 11, 2026, 11:08 AM CST

Added on Sep 11, 2026, 11:12 AM CST

Added by Jared videogain



[20260911_110813_photo.jpeg](#)

Added as Reference

Taken on Sep 11, 2026, 11:08 AM CST

Added on Sep 11, 2026, 11:12 AM CST

Added by Jared videgain



[20260911_110757_photo.jpeg](#)

Added as Reference

Taken on Sep 11, 2026, 11:07 AM CST

Added on Sep 11, 2026, 11:12 AM CST

Added by Jared videgain

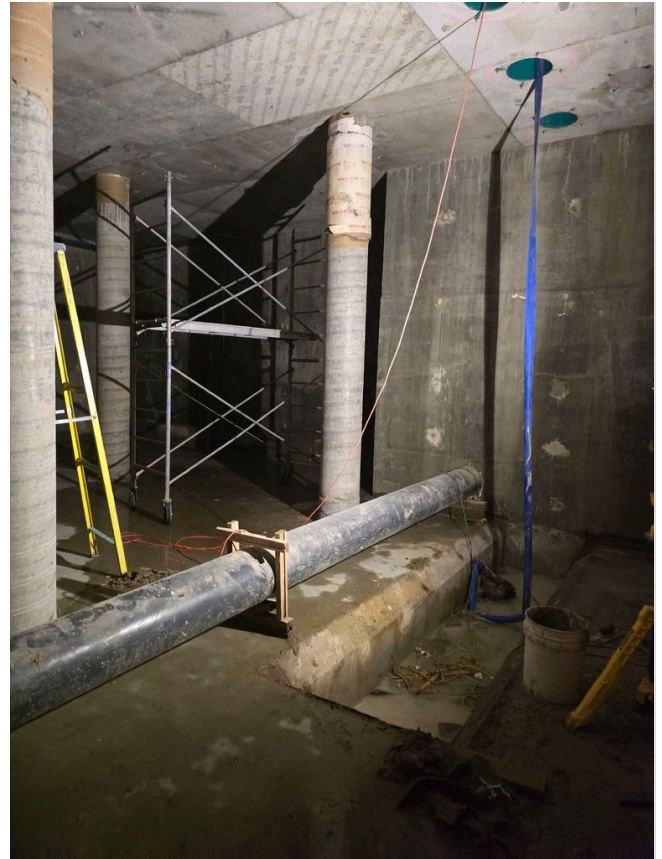
[20260911_110805_photo.jpeg](#)

Added as Reference

Taken on Sep 11, 2026, 11:08 AM CST

Added on Sep 11, 2026, 11:12 AM CST

Added by Jared videogain

[20260911_110859_photo.jpeg](#)

Added as Reference

Taken on Sep 11, 2026, 11:08 AM CST

Added on Sep 11, 2026, 11:12 AM CST

Added by Jared videogain

6. Saturday/Sunday

6.1 Date
September 12 - 13, 2026

6.2 Work Completed
N/A

Notes

Week Look Ahead:

- Finish painting of ceiling
- Mechanical piping and install of unit heaters
- Mechanical pad formwork and reinforcing
- Pile install for loading bay grade beam
- Interior trusscore install
- Break down and remove old roof from site
- Preparation of windows for install

- Clean out waste chamber
- Review lifting beam plan for install
