

Form detail

#144: Weekly Report #22 - September 14 - 20, 2026



Forms

Location	
Form date	Sep 21, 2026
Template	Project Status Report
Description	Redvers WTP Upgrade - Weekly Report #22
Due date	Oct 1, 2026
Submitted by	Jordan Gent
Submitter's company	CCR Construction Ltd
Status	Closed
Last update	Oct 1, 2026, 4:56 PM CST
Last updated by	Jordan Gent
Included references	Assets Files Forms Issues Photos File Packages Sheets Submittals RFIs PCOs Schedule Activities

1. Monday

- 1.1 Date
September 14, 2026
- 1.2 Work Completed
Layout of access hatch work, installing interior wall sheathing, painting of ceiling, piping and running gas line

Photos (3)

[20260914_171329_photo.jpeg](#)

Added as Reference

Taken on Sep 14, 2026, 5:13 PM CST

Added on Sep 14, 2026, 5:29 PM CST

Added by Jared videogain




[20260914_171441_photo.jpeg](#)

Added as Reference

Taken on Sep 14, 2026, 5:14 PM CST

Added on Sep 14, 2026, 5:29 PM CST

Added by Jared videogain

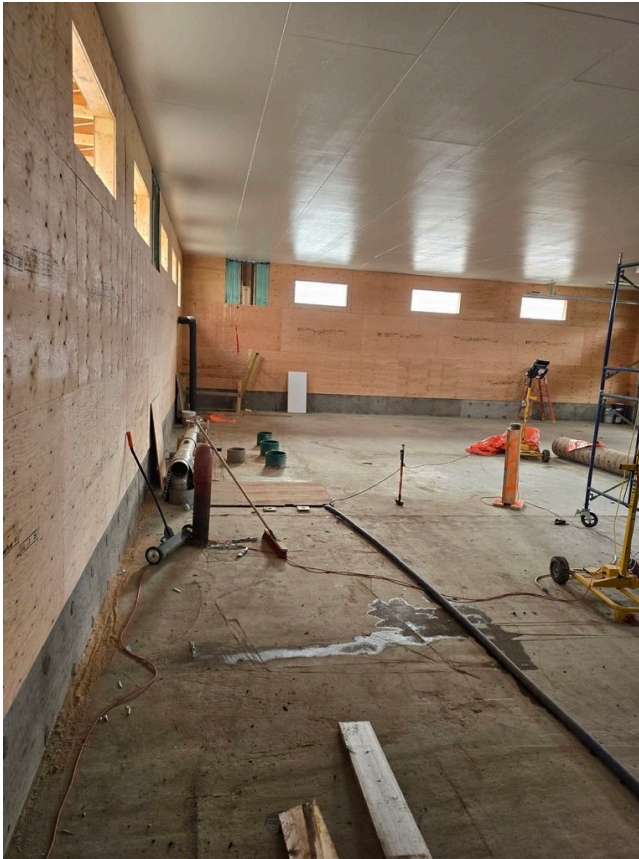

[20260914_171443_photo.jpeg](#)

Added as Reference

Taken on Sep 14, 2026, 5:14 PM CST

Added on Sep 14, 2026, 5:29 PM CST

Added by Jared videogain

2. Tuesday

2.1 Date

September 15, 2026

2.2 Work Completed

Installing piles for the loading dock grade beam, formwork for meachanical maintenance pads, piping and installing gas line with unit heaters, spray foam in roof trusses

Photos (3)


[20260915_114906_photo.jpeg](#)

Added as Reference

Taken on Sep 15, 2026, 11:49 AM CST

Added on Sep 15, 2026, 5:35 PM CST

Added by Jared videogain

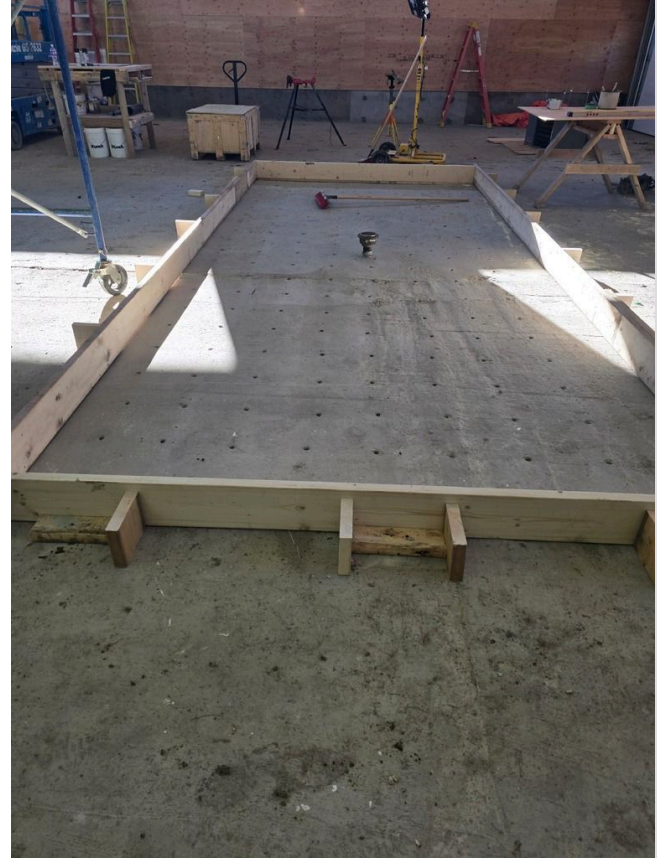

[20260915_170726_photo.jpeg](#)

Added as Reference

Taken on Sep 15, 2026, 5:07 PM CST

Added on Sep 15, 2026, 5:35 PM CST

Added by Jared videogain



[20260915_170715_photo.jpeg](#)

Added as Reference

Taken on Sep 15, 2026, 5:07 PM CST

Added on Sep 15, 2026, 5:35 PM CST

Added by Jared videogain

3. Wednesday

3.1 Date

September 16, 2026

3.2 Work Completed

Working on installing dowels for mechanical maintenance pad, spray foam in roof trusses, installing piping and gas line with unit heaters

4. Thursday

4.1 Date

September 17, 2026

4.2 Work Completed

Prepare window frames for install, clean out waste chamber for plumbers, demo old roof and remove from site, piping and gas line install

Photos (4)




[20260917_154513_photo.jpeg](#)

Added as Reference

Taken on Sep 17, 2026, 3:45 PM CST

Added on Sep 17, 2026, 6:17 PM CST

Added by Jared videogain

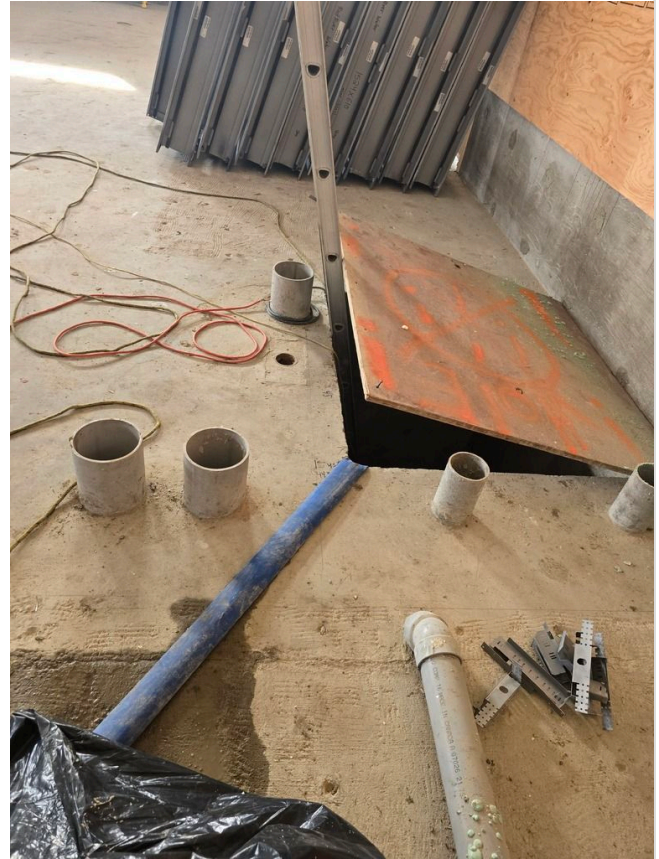


[20260917_154640_photo.jpeg](#)

Added as Reference

Taken on Sep 17, 2026, 3:46 PM CST

Added on Sep 17, 2026, 6:17 PM CST

Added by Jared videogain

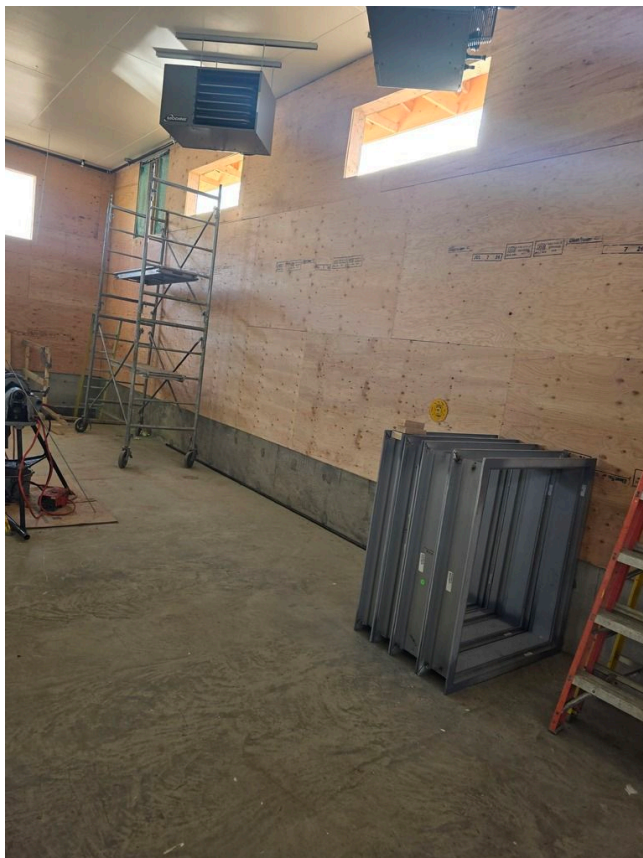
[20260917_154524_photo.jpeg](#)

Added as Reference

Taken on Sep 17, 2026, 3:45 PM CST

Added on Sep 17, 2026, 6:17 PM CST

Added by Jared videogain

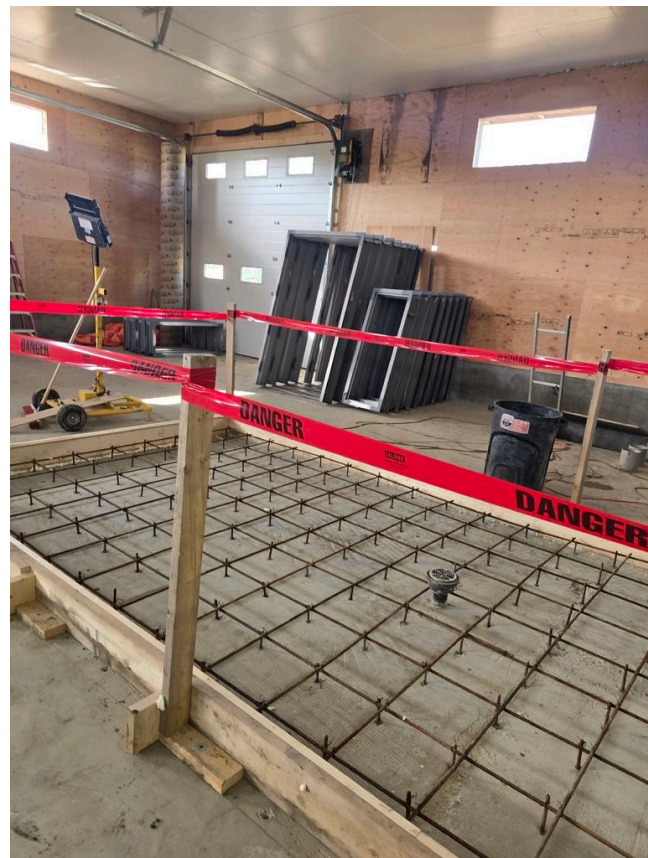[20260917_154502_photo.jpeg](#)

Added as Reference

Taken on Sep 17, 2026, 3:45 PM CST

Added on Sep 17, 2026, 6:17 PM CST

Added by Jared videogain

5. Friday

- 5.1 Date
September 18, 2026
- 5.2 Work Completed
Review of lifting beam plan for install next week

6. Saturday/Sunday

- 6.1 Date
September 19-20, 2026
- 6.2 Work Completed
N/A

Notes

Week Look Ahead:

- Install windows
- Install lifting beam
- Install trusscore
- Finish gas line install
