

Form detail

#145: Weekly Report #23 - September 21 - 27, 2026

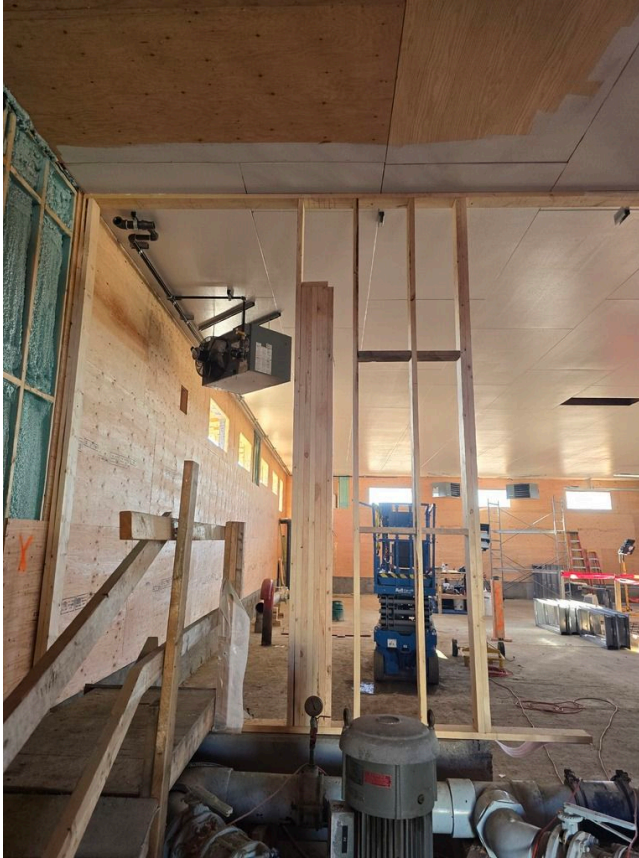


Forms

Location	
Form date	Sep 28, 2026
Template	Project Status Report
Description	Redvers WTP Upgrade - Weekly Report #23
Due date	
Submitted by	Jordan Gent
Submitter's company	CCR Construction Ltd
Status	Closed
Last update	Oct 2, 2026, 10:43 AM CST
Last updated by	Jordan Gent
Included references	Assets Files Forms Issues Photos File Packages Sheets Submittals RFIs PCOs Schedule Activities

1. Monday

- 1.1 Date
September 21, 2026
- 1.2 Work Completed
Install windows, clean out waste chamber, modify columns for beam install

Photos (3)

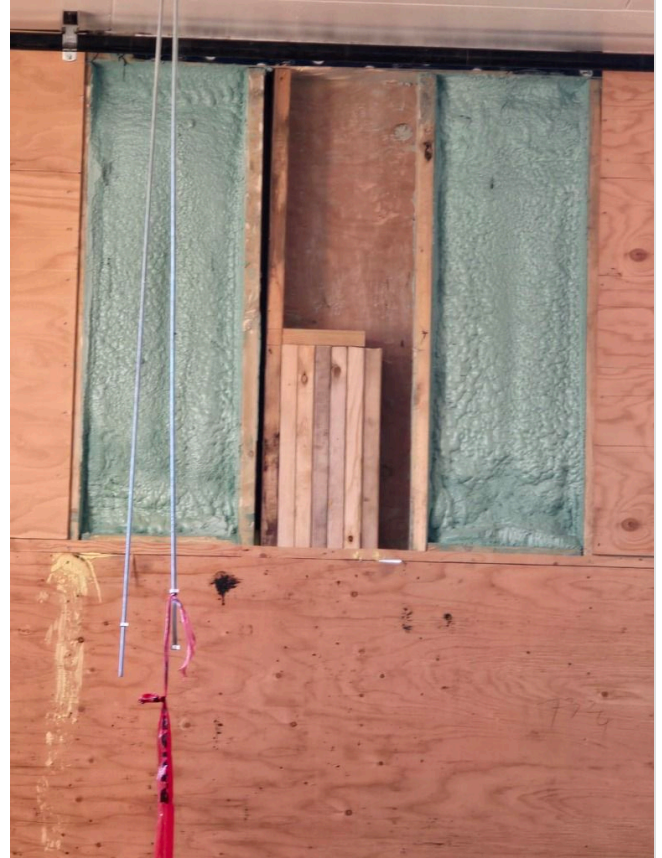
[20260921_164933_photo.jpeg](#)

Added as Reference

Taken on Sep 21, 2026, 4:49 PM CST

Added on Sep 21, 2026, 4:58 PM CST

Added by Jared videogain



[20260921_164949_photo.jpeg](#)

Added as Reference

Taken on Sep 21, 2026, 4:49 PM CST

Added on Sep 21, 2026, 4:58 PM CST

Added by Jared videogain



[20260921_164909_photo.jpeg](#)

Added as Reference

Taken on Sep 21, 2026, 4:49 PM CST

Added on Sep 21, 2026, 4:58 PM CST

Added by Jared videogain

2. Tuesday

2.1 Date

September 22, 2026

2.2 Work Completed

Install windows, install lifting beam, clean up site, interior trusscore install, install gas line.

Photos (3)

[20260922_185226_photo.jpeg](#)

Added as Reference

Taken on Sep 22, 2026, 6:52 PM CST

Added on Sep 22, 2026, 7:00 PM CST

Added by Jared videogain



[20260922_185231_photo.jpeg](#)

Added as Reference

Taken on Sep 22, 2026, 6:52 PM CST

Added on Sep 22, 2026, 7:00 PM CST

Added by Jared videogain



[20260922_185234_photo.jpeg](#)

Added as Reference

Taken on Sep 22, 2026, 6:52 PM CST

Added on Sep 22, 2026, 7:00 PM CST

Added by Jared videogain

3. Wednesday

3.1 Date

September 23, 2026

3.2 Work Completed

Install windows, lifting beam install, gas line install, trusscore install

Photos (4)

[20260923_172720_photo.jpeg](#)

Added as Reference

Taken on Sep 23, 2026, 5:27 PM CST

Added on Sep 23, 2026, 5:32 PM CST

Added by Jared videgain



[20260923_172545_photo.jpeg](#)

Added as Reference

Taken on Sep 23, 2026, 5:25 PM CST

Added on Sep 23, 2026, 5:32 PM CST

Added by Jared videgain

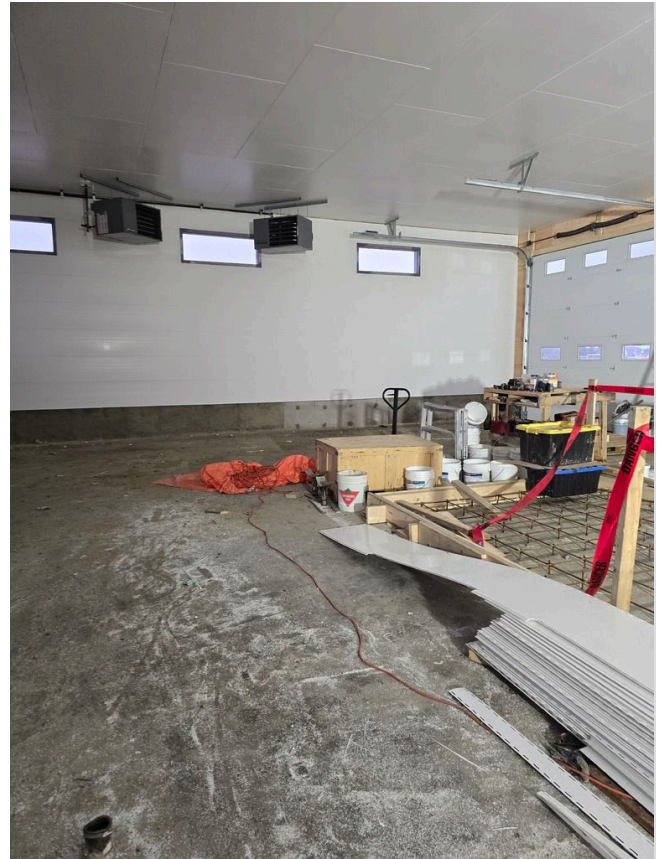
[20260923_172552_photo.jpeg](#)

Added as Reference

Taken on Sep 23, 2026, 5:25 PM CST

Added on Sep 23, 2026, 5:32 PM CST

Added by Jared videogain

[20260923_172548_photo.jpeg](#)

Added as Reference

Taken on Sep 23, 2026, 5:25 PM CST

Added on Sep 23, 2026, 5:32 PM CST

Added by Jared videogain

4. Thursday

- 4.1 Date
September 24, 2026
- 4.2 Work Completed
Install windows, clean up site and move in fencing, install exterior door, install gas line.

5. Friday

- 5.1 Date
September 25, 2026
- 5.2 Work Completed
N/A

6. Saturday/Sunday

6.1 Date
September 26 - 27, 2026

6.2 Work Completed
N/A

Notes

Week Look Ahead:

- Install exterior doors
- Finish interior trusscore install
- Cladding on exterior
- Form remaining mechanical maintenance pads
- Formwork for access hatches
- Chip concrete around hatches
