

Form detail

#147: Weekly Report #24 - September 28 - October 4, 2026



Forms

Location	
Form date	Oct 2, 2026
Template	Project Status Report
Description	Redvers WTP Upgrade - Weekly Report #24
Due date	Oct 2, 2026
Submitted by	Jordan Gent
Submitter's company	CCR Construction Ltd
Status	Closed
Last update	Oct 2, 2026, 12:44 PM CST
Last updated by	Jordan Gent
Included references	Assets Files Forms Issues Photos File Packages Sheets Submittals RFIs PCOs Schedule Activities

1. Monday

- 1.1 Date
September 28, 2026
- 1.2 Work Completed
Door install, removal of exterior ramp, access hatch formwork, finish installing trusscore on interior

Photos (1)

[20260928_151038_photo.jpeg](#)

Added as Reference

Taken on Sep 28, 2026, 3:10 PM CST

Added on Sep 28, 2026, 5:35 PM CST

Added by Jared videogain


2. Tuesday

2.1 Date

September 29, 2026

2.2 Work Completed

Form and drill dowels for mechanical maintenance pads, formwork for access hatches, flashing on exterior brick ledge

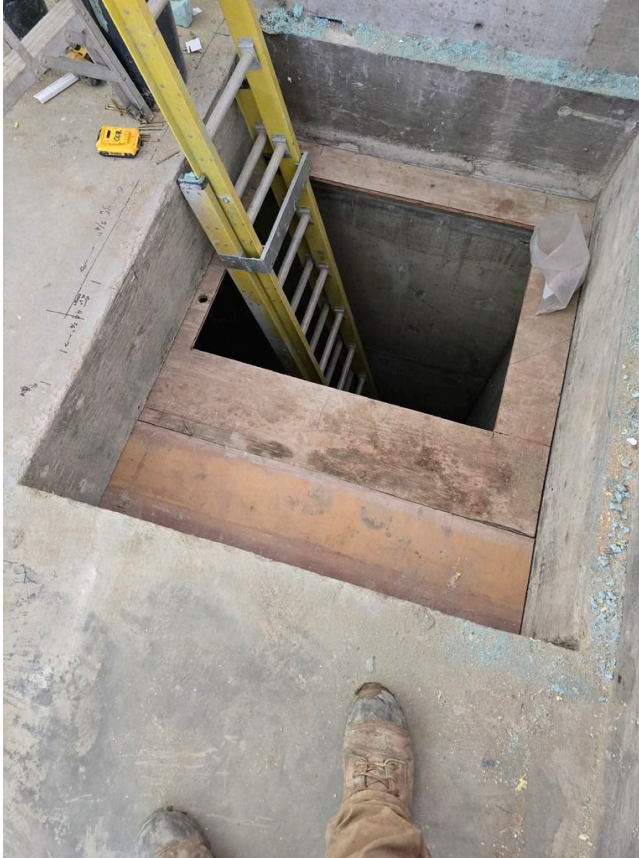Photos (5)


[20260929_172507_photo.jpeg](#)

Added as Reference

Taken on Sep 29, 2026, 5:25 PM CST

Added on Sep 29, 2026, 5:46 PM CST

Added by Jared videogain

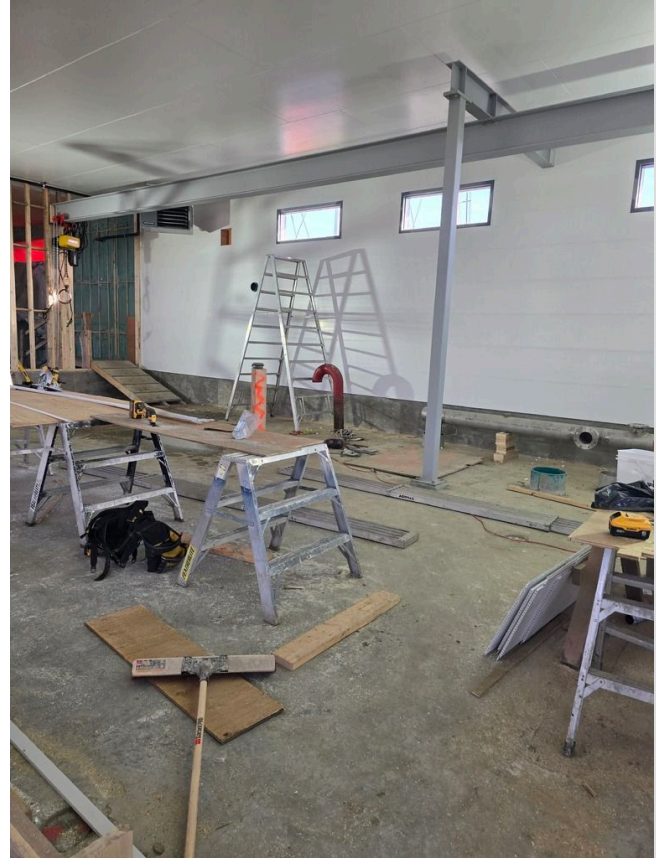

[20260929_172428_photo.jpeg](#)

Added as Reference

Taken on Sep 29, 2026, 5:24 PM CST

Added on Sep 29, 2026, 5:46 PM CST

Added by Jared videogain



[20260929_172434_photo.jpeg](#)

Added as Reference

Taken on Sep 29, 2026, 5:24 PM CST

Added on Sep 29, 2026, 5:46 PM CST

Added by Jared videgain



[20260929_120504_photo.jpeg](#)

Added as Reference

Taken on Sep 29, 2026, 12:05 PM CST

Added on Sep 29, 2026, 5:46 PM CST

Added by Jared videgain



[20260929_130025_photo.jpeg](#)

Added as Reference

Taken on Sep 29, 2026, 1:00 PM CST

Added on Sep 29, 2026, 5:46 PM CST

Added by Jared videogain


3. Wednesday

3.1 Date

September 30, 2026

3.2 Work Completed

Access hatch formwork, louver install and sleeves for unit heater exhausts, exterior cladding

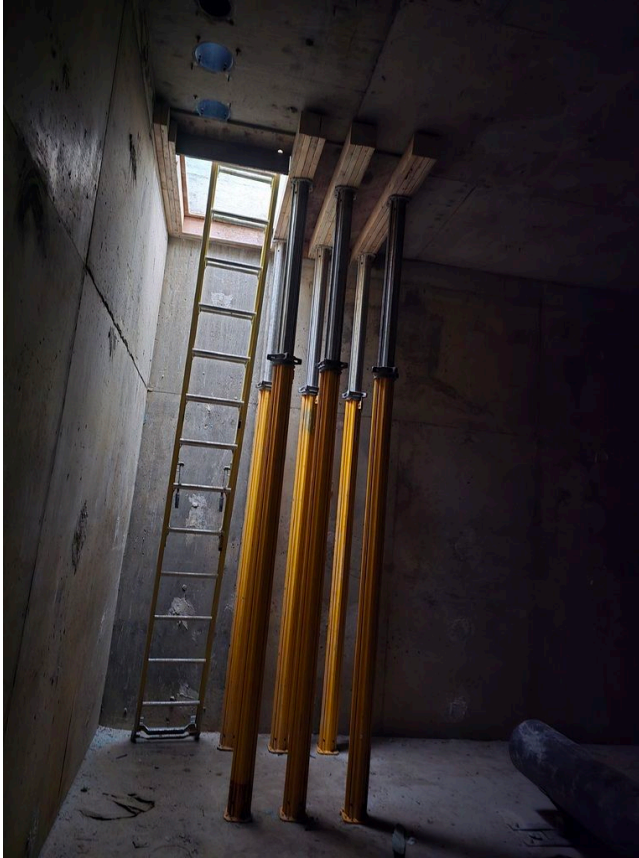Photos (1)

[20260930_162558_photo.jpeg](#)

Added as Reference

Taken on Sep 30, 2026, 4:25 PM CST

Added on Sep 30, 2026, 5:09 PM CST

Added by Jared videogain

4. Thursday

4.1 Date

October 1, 2026

4.2 Work Completed

Exterior cladding install, formwork for access hatches

Photos (6)

[20261001_152457_photo.jpeg](#)

Added as Reference

Taken on Oct 1, 2026, 3:24 PM CST

Added on Oct 1, 2026, 3:38 PM CST

Added by Jared videogain




[20261001_152508_photo.jpeg](#)

Added as Reference

Taken on Oct 1, 2026, 3:25 PM CST

Added on Oct 1, 2026, 3:38 PM CST

Added by Jared videogain

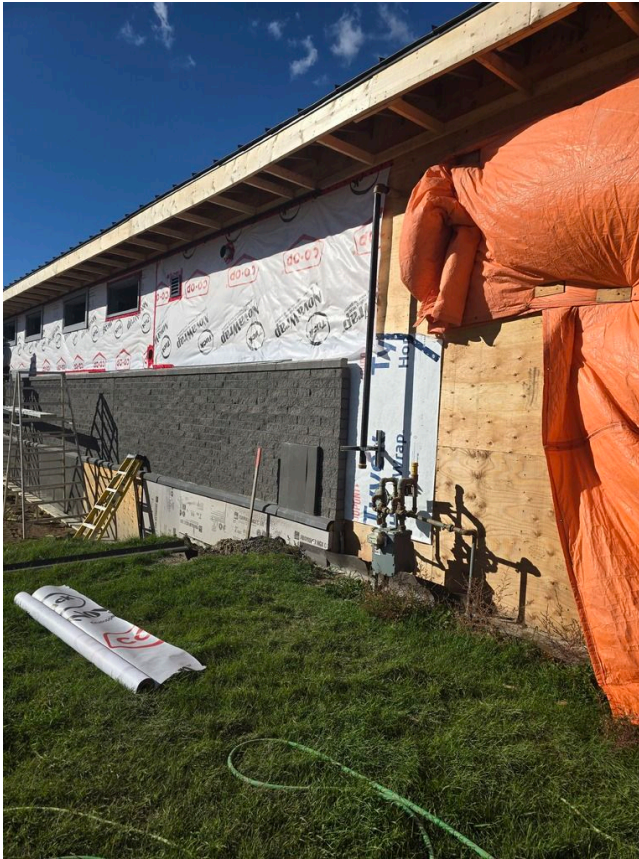


[20261001_152405_photo.jpeg](#)

Added as Reference

Taken on Oct 1, 2026, 3:24 PM CST

Added on Oct 1, 2026, 3:38 PM CST

Added by Jared videgain

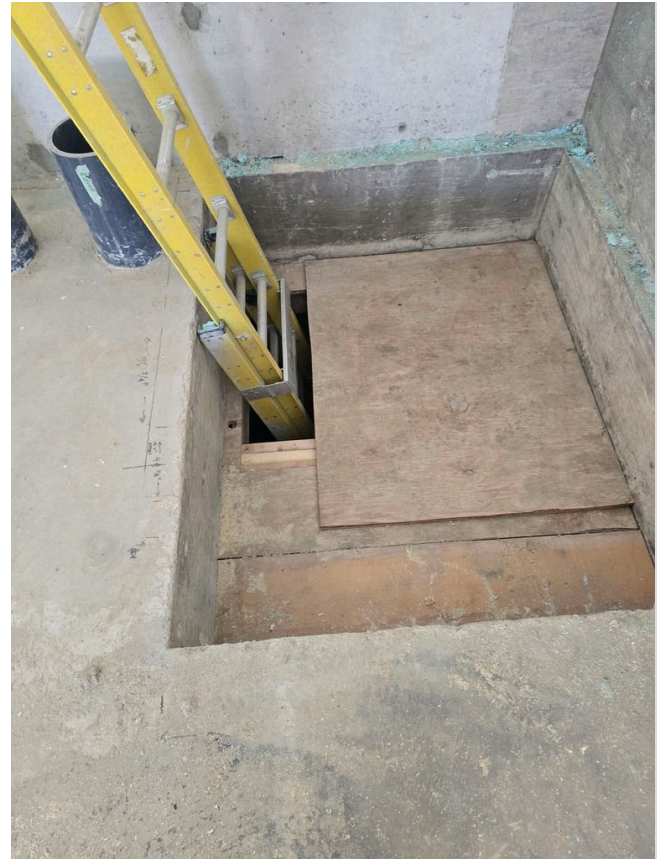


[20261001_152441_photo.jpeg](#)

Added as Reference

Taken on Oct 1, 2026, 3:24 PM CST

Added on Oct 1, 2026, 3:38 PM CST

Added by Jared videgain

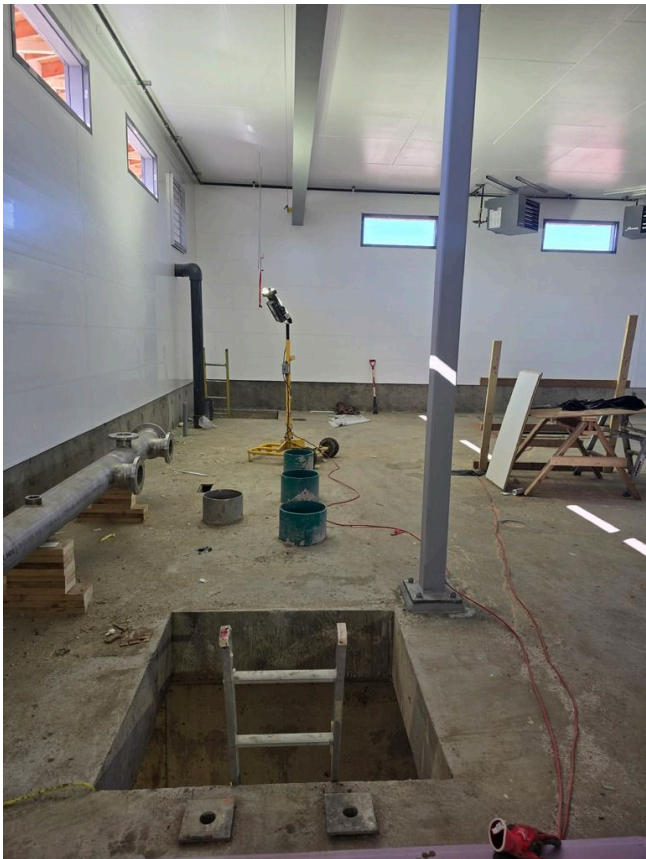

[20261001_105050_photo.jpeg](#)
Added as Reference
Taken on Oct 1, 2026, 10:50 AM CST
Added on Oct 1, 2026, 3:38 PM CST
Added by Jared videogain



[20261001_152451_photo.jpeg](#)
Added as Reference
Taken on Oct 1, 2026, 3:24 PM CST
Added on Oct 1, 2026, 3:38 PM CST
Added by Jared videogain

5. Friday

- 5.1 Date
 October 2, 2026
- 5.2 Work Completed
 N/A

6. Saturday/Sunday

- 6.1 Date
 October 3-4, 2026
- 6.2 Work Completed
 N/A

Notes

Week Look Ahead:

- Access hatch install
- Loading dock grade beam formwork and reinforcing
- Cleaning reservoir
- Patch reservoir holes in waste chamber
- Painting window/door frames
- Install exterior cladding
- Install remaining exterior door frames
- Glazing install
