

Form detail

#22: Weekly Report May 11 - May 17, 2026




Forms


Location	
Form date	May 12, 2026
Template	Daily Log
Description	
Due date	
Created by	kurt kurt
Status	In progress
Last update	May 15, 2026, 7:52 AM CST
Last updated by	kurt kurt
Included references	Assets Files Forms Issues Photos File Packages Sheets Submittals RFIs PCOs Schedule Activities


Weather

🌧️ Rain: 0.00 inches

🍏 Weather [View Sources](#)

7:00 AM **Clear**
 Temperature: 50°F
 Wind: 📏 13mph
 Humidity: 72%

12:00 PM **Windy**
 Temperature: 67°F
 Wind: ↓ 19mph
 Humidity: 30%

4:00 PM **Windy**
 Temperature: 71°F
 Wind: 📏 15mph
 Humidity: 26%

Updated May 12, 2026 at 7:04 PM

1. Companies On-Site & Manpower

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	CCR Construction	-	2	-	-	- Install safety fence - Drill and epoxy dowels - remove existing siding - pressure wash existing wall mud off
-	Moskal Mechanical	-	5	-	-	- Mobilize material to site - Core the two holes into existing reservoir - install sleeves into new wall forms
-	Rez Rods	-	5	-	-	- Install wall reinforcing
-	HB Foundations	-	3	-	-	- building forms to close walls up after reinforcing is inspected.
-	General Hydrovac	-	1	-	-	- Pumping remaining water from existing reservoir.
Totals:			16	0	0	

2. Materials & Shipping

Material	Quantity	Unit	Comment
----------	----------	------	---------

3. Equipment

Equipment	Quantity	Hours used	Comment
-----------	----------	------------	---------

4. Important Conversations

4.1 Document all important information / discussions / dates.

Next Week Look Ahead

- inspecting the reinforcing for the walls
- close up walls with outside forms
- install slab dowels
- pour foundation walls
- continue demolition of existing building envelope
- remove and support existing mechanical/electrical in building

Photos (15)



[IMG_1160.jpeg](#)

Added as Reference

Taken on May 11, 2026, 11:02 AM CST

Added on May 12, 2026, 8:44 AM CST

Added by kurt kurt



[IMG_1164.jpeg](#)

Added as Reference

Taken on May 11, 2026, 11:54 AM CST

Added on May 12, 2026, 8:44 AM CST

Added by kurt kurt




[IMG_1158.jpeg](#)

Added as Reference

Taken on May 11, 2026, 10:57 AM CST

Added on May 12, 2026, 8:44 AM CST

Added by kurt kurt

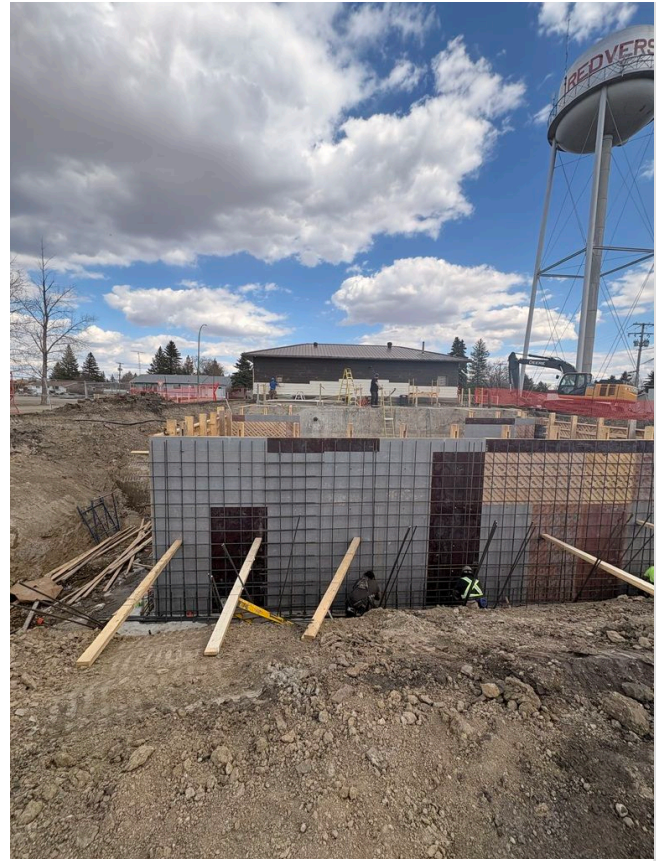

[IMG_1195.jpeg](#)

Added as Reference

Taken on May 12, 2026, 3:00 PM CST

Added on May 12, 2026, 6:41 PM CST

Added by kurt kurt




[IMG_1186.jpeg](#)

Added as Reference

Taken on May 12, 2026, 1:04 PM CST

Added on May 12, 2026, 6:41 PM CST

Added by kurt kurt

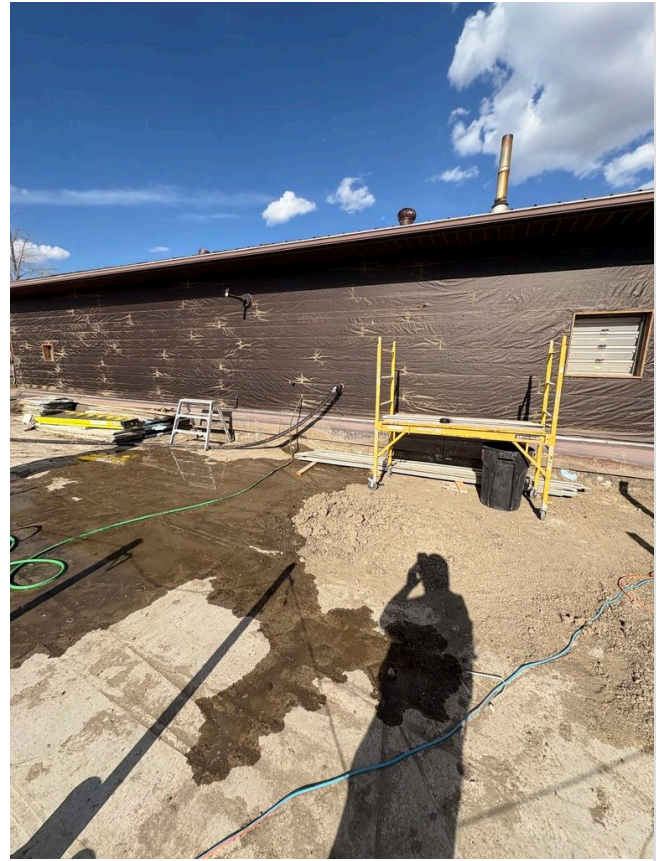

[IMG_1200.jpeg](#)

Added as Reference

Taken on May 12, 2026, 5:02 PM CST

Added on May 12, 2026, 6:41 PM CST

Added by kurt kurt



[IMG_1196.jpeg](#)

Added as Reference

Taken on May 12, 2026, 3:37 PM CST

Added on May 12, 2026, 6:41 PM CST

Added by kurt kurt



[IMG_1199.jpeg](#)

Added as Reference

Taken on May 12, 2026, 5:02 PM CST

Added on May 12, 2026, 6:40 PM CST

Added by kurt kurt




[IMG_1236.jpeg](#)

Added as Reference

Taken on May 13, 2026, 4:50 PM CST

Added on May 13, 2026, 6:46 PM CST

Added by kurt kurt

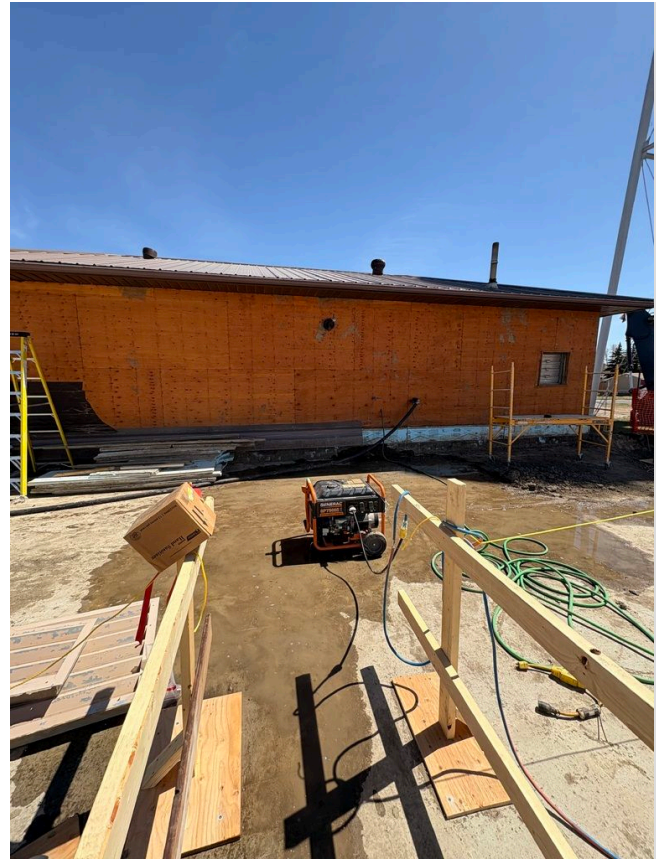

[IMG_1224.jpeg](#)

Added as Reference

Taken on May 13, 2026, 12:11 PM CST

Added on May 13, 2026, 1:49 PM CST

Added by kurt kurt




[IMG_1217.jpeg](#)

Added as Reference

Taken on May 13, 2026, 9:36 AM CST

Added on May 13, 2026, 1:49 PM CST

Added by kurt kurt

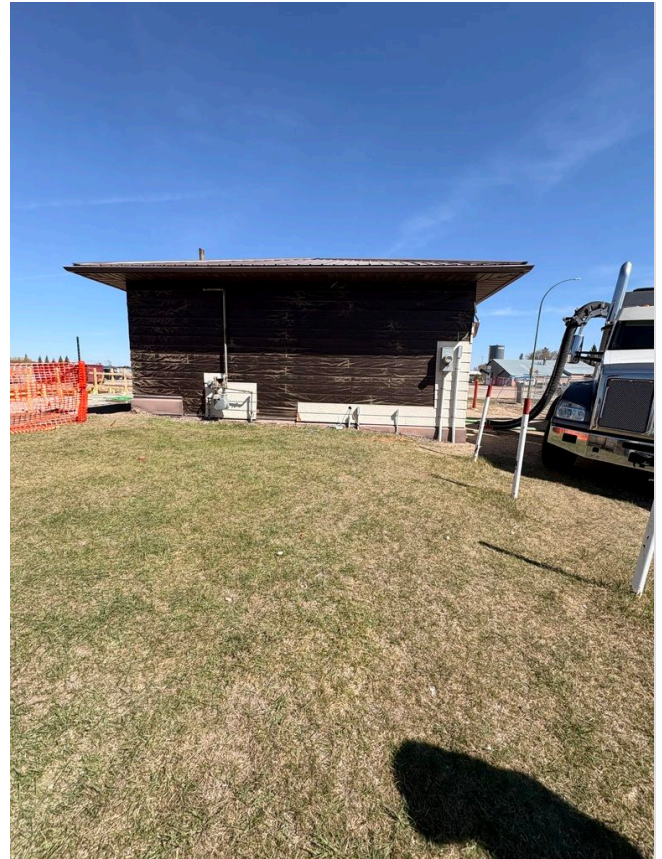

[IMG_1219.jpeg](#)

Added as Reference

Taken on May 13, 2026, 10:11 AM CST

Added on May 13, 2026, 1:49 PM CST

Added by kurt kurt




[IMG_1175.jpeg](#)

Added as Reference

Taken on May 12, 2026, 8:24 AM CST

Added on May 12, 2026, 6:41 PM CST

Added by kurt kurt

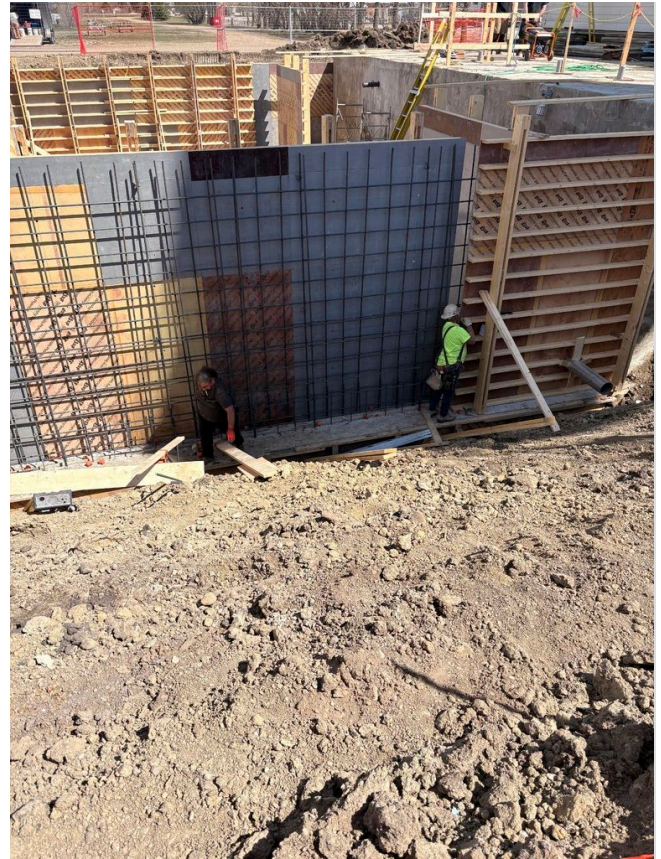

[IMG_1180.jpeg](#)

Added as Reference

Taken on May 12, 2026, 10:55 AM CST

Added on May 12, 2026, 6:41 PM CST

Added by kurt kurt



[IMG_1212.jpeg](#)

Added as Reference

Taken on May 13, 2026, 8:00 AM CST

Added on May 13, 2026, 1:48 PM CST

Added by kurt kurt
