

Form detail

#16: Weekly Report May 4 - 11, 2026




Forms


Location	
Form date	May 5, 2026
Template	Daily Log
Description	Weekly report for client/consultant
Due date	
Created by	kurt kurt
Status	In progress
Last update	May 7, 2026, 11:20 PM CST
Last updated by	kurt kurt
Included references	Assets Files Forms Issues Photos File Packages Sheets Submittals RFIs PCOs Schedule Activities


Weather

🌧️ Rain: 0.00 inches

🍏 Weather [View Sources](#)

7:00 AM **Partly Cloudy**
 Temperature: 30°F
 Wind: 📏 12mph
 Humidity: 72%

12:00 PM **Windy**
 Temperature: 35°F
 Wind: ↓ 16mph
 Humidity: 50%

4:00 PM **Windy**
 Temperature: 39°F
 Wind: ↓ 15mph
 Humidity: 42%

Updated May 7, 2026 at 8:33 AM

1. Companies On-Site & Manpower

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	CCR Construction	-	3	-	-	<ul style="list-style-type: none"> - Supervision - Snow fence install around excavation. - Repair site fencing from windstorm, added more bracing. - Hooked up temp power for site trailer. - site clean up. - Wet cure slab.
-	HB Foundations	-	9	-	-	<ul style="list-style-type: none"> - Form sump pits. - Install keyway and water stop. - Pour and finish base slab. - prep and install wall forms.
-	Moskal Mechanical	-	1	-	-	<ul style="list-style-type: none"> - Installing sump pit pipe for weeping tile install. - Mobilize telehandler and sea-can. -Repair existing water line for campground.
-	Five Star Pumping	-	1	-	-	<ul style="list-style-type: none"> - Pumping concrete for base slab.
-	Parkland Geo	-	1	-	-	<ul style="list-style-type: none"> - Testing concrete for base slab.
-	Johnston Concrete	-	6	-	-	<ul style="list-style-type: none"> - Deliver concrete for base slab.
-	National Crane	-	1	6	-	<ul style="list-style-type: none"> - Crane wall forms in place
Totals:			22	6	0	

2. Materials & Shipping

Material	Quantity	Unit	Comment
32MPA concrete	76	m ³	

3. Equipment

Equipment	Quantity	Hours used	Comment
Telehandler	1	0	
Sea-can	1	0	30 foot

4. Important Conversations

- 4.1 Document all important information / discussions / dates.
Look ahead for week of May 11, 2026 - May 15, 2026

- **Installing reinforcing for walls**
- **Installing transfer pipe from existing reservoir to new reservoir which will require draining the existing reservoir to complete the work, once it is empty the existing reservoir will be hydrovac to remove any sludge build up at the bottom prior to filling.**
- **exterior siding demo will start**
- **selective interior demo to start**
- **Mechanical penetrations will be installed in forms**
- **Moskal will be mobilizing materials and sea can to site.**

Photos (18)



[IMG_0887.jpeg](#)

Added as Reference

Taken on May 4, 2026, 11:44 AM CST

Added on May 4, 2026, 11:57 AM CST

Added by kurt kurt



[IMG_0879.jpeg](#)

Added as Reference

Taken on May 4, 2026, 11:42 AM CST

Added on May 4, 2026, 11:57 AM CST

Added by kurt kurt



[IMG_0932.jpeg](#)

Added as Reference

Taken on May 5, 2026, 8:43 AM CST

Added on May 5, 2026, 10:06 AM CST

Added by kurt kurt



[IMG_0931.jpeg](#)

Added as Reference

Taken on May 5, 2026, 8:43 AM CST

Added on May 5, 2026, 10:06 AM CST

Added by kurt kurt




[IMG_0930.jpeg](#)

Added as Reference

Taken on May 5, 2026, 8:43 AM CST

Added on May 5, 2026, 10:06 AM CST

Added by kurt kurt

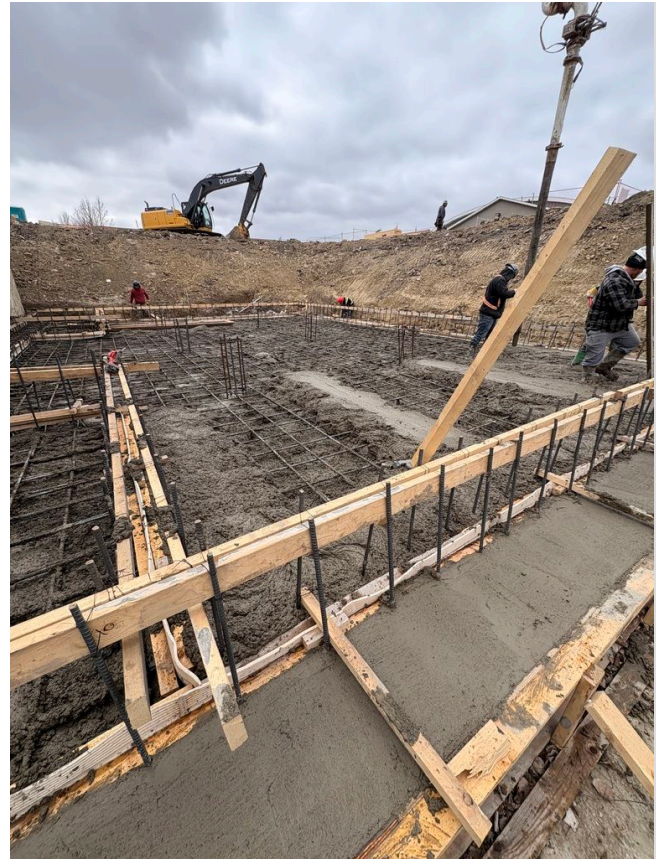

[IMG_0947.jpeg](#)

Added as Reference

Taken on May 5, 2026, 11:09 AM CST

Added on May 5, 2026, 1:29 PM CST

Added by kurt kurt



[IMG_0956.jpeg](#)

Added as Reference

Taken on May 5, 2026, 1:48 PM CST

Added on May 5, 2026, 3:03 PM CST

Added by kurt kurt



[IMG_0954.jpeg](#)

Added as Reference

Taken on May 5, 2026, 12:51 PM CST

Added on May 5, 2026, 3:03 PM CST

Added by kurt kurt



[IMG_0975.jpeg](#)

Added as Reference

Taken on May 5, 2026, 4:22 PM CST

Added on May 5, 2026, 4:26 PM CST

Added by kurt kurt



[IMG_0974.jpeg](#)

Added as Reference

Taken on May 5, 2026, 4:14 PM CST

Added on May 5, 2026, 4:26 PM CST

Added by kurt kurt



[1000035997.JPG](#)

Added as Reference

Added on May 6, 2026, 2:47 PM CST

Added by kurt kurt



[IMG_0971.jpeg](#)

Added as Reference

Taken on May 5, 2026, 3:42 PM CST

Added on May 5, 2026, 4:26 PM CST

Added by kurt kurt



[IMG_0983.jpeg](#)

Added as Reference

Taken on May 6, 2026, 8:50 AM CST

Added on May 6, 2026, 10:24 AM CST

Added by kurt kurt



[IMG_1106.jpeg](#)

Added as Reference

Taken on May 7, 2026, 1:06 PM CST

Added on May 7, 2026, 10:00 PM CST

Added by kurt kurt



[IMG_1046.jpeg](#)

Added as Reference

Taken on May 7, 2026, 9:39 AM CST

Added on May 7, 2026, 10:00 PM CST

Added by kurt kurt




[IMG_1107.jpeg](#)

Added as Reference

Taken on May 7, 2026, 1:06 PM CST

Added on May 7, 2026, 10:00 PM CST

Added by kurt kurt

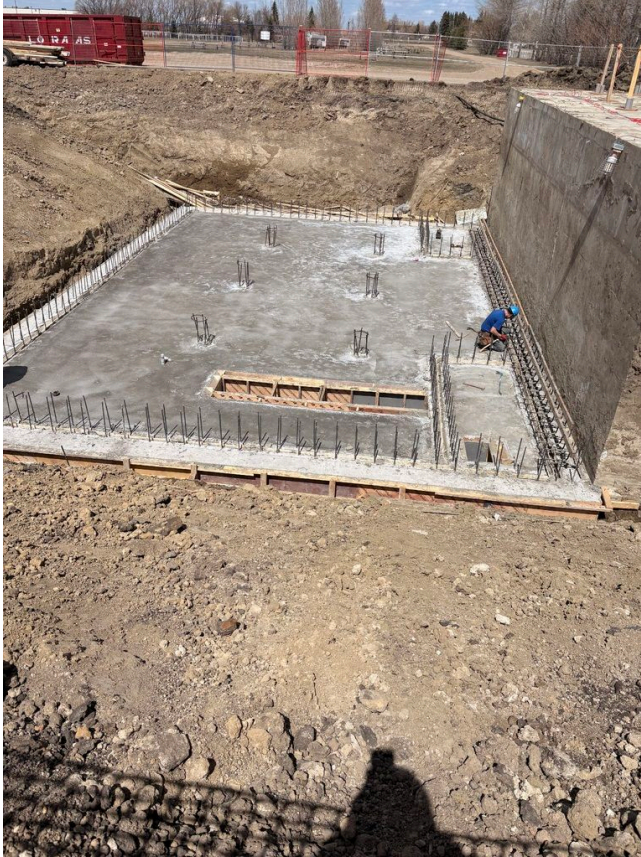

[IMG_1012.jpeg](#)

Added as Reference

Taken on May 6, 2026, 1:00 PM CST

Added on May 6, 2026, 1:48 PM CST

Added by kurt kurt



[IMG_1049.jpeg](#)

Added as Reference

Taken on May 7, 2026, 10:22 AM CST

Added on May 7, 2026, 10:00 PM CST

Added by kurt kurt
