

Form detail

#77: Weekly Report # 13 July 13 - July 20, 2026



Forms

Location

Form date Jul 16, 2026

Template Daily Log

Description Redvers WTP - Weekly Report # 13

Due date

Created by kurt kurt

Status In progress

Last update Jul 16, 2026, 12:45 PM CST

Last updated by kurt kurt

Included references Assets | Files | Forms | Issues | Photos | File Packages | Sheets | Submittals | RFIs | PCOs | Schedule Activities

Weather

Rain: 0.13 inches

Weather [View Sources](#)

7:00 AM Cloudy
 Temperature: 62°F
Wind: ← 11mph
Humidity: 94%

12:00 PM Cloudy
 Temperature: 72°F
Wind: ← 6mph
Humidity: 82%

4:00 PM Mostly Cloudy
 Temperature: 75°F
Wind: ↘ 7mph
Humidity: 79%

Updated Jul 17, 2026 at 10:12 AM

1. Companies On-Site & Manpower

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	CCR Construction	-	3	-	-	- drilled dowels for curb modification - built walkway into the overhead door - braced existing piping in the building
-	HB Foundations	-	5	-	-	- patch and plug holes in reservoir - site clean up - demobilize materials
-	TNA Construction	-	5	-	-	- Installing truss blocking - Installing joist hangers - Framing walls - Installed roof sheathing - Installed roof trusses
-	Flying G Crane	-	2	-	-	- Crane roof trusses up
Totals:			15	0	0	

2. Materials & Shipping

Material	Quantity	Unit	Comment
----------	----------	------	---------

3. Equipment

Equipment	Quantity	Hours used	Comment
-----------	----------	------------	---------

4. Important Conversations

- 4.1 Document all important information / discussions / dates.
Look ahead for the week of July 20-July 26, 2026

CCR

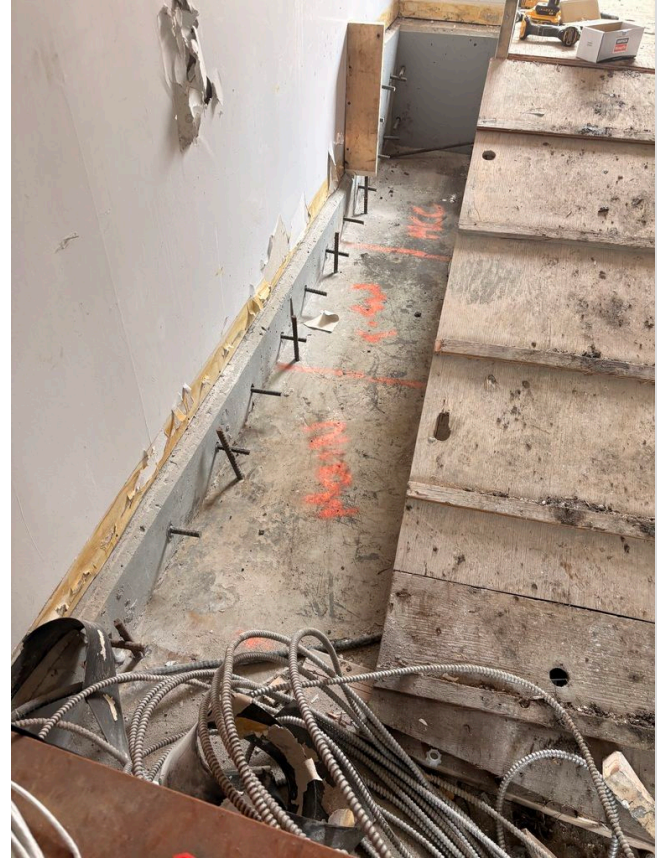
- Install footing base (weather permitting)
- Hydrostatic testing reservoir
- Strip curb extension forms
- Miscellaneous tasks

HB Foundations

- Patch tie holes
- Site clean up

T&A Construction

- Frame walls on ground
- Sheet the new building roof

Photos (15)[IMG_2701.jpeg](#)**Added as** Reference**Taken on** Jul 15, 2026, 4:33 PM CST**Added on** Jul 15, 2026, 6:01 PM CST**Added by** kurt kurt[IMG_2692.jpeg](#)**Added as** Reference**Taken on** Jul 15, 2026, 3:43 PM CST**Added on** Jul 15, 2026, 6:01 PM CST**Added by** kurt kurt

[IMG_2687.jpeg](#)

Added as Reference

Taken on Jul 15, 2026, 2:53 PM CST

Added on Jul 15, 2026, 3:35 PM CST

Added by kurt kurt

[IMG_2683.jpeg](#)

Added as Reference

Taken on Jul 15, 2026, 2:51 PM CST

Added on Jul 15, 2026, 3:34 PM CST

Added by kurt kurt

[IMG_2685.jpeg](#)

Added as Reference

Taken on Jul 15, 2026, 2:51 PM CST

Added on Jul 15, 2026, 3:34 PM CST

Added by kurt kurt

[IMG_2669.jpeg](#)

Added as Reference

Taken on Jul 15, 2026, 1:38 PM CST

Added on Jul 15, 2026, 3:24 PM CST

Added by kurt kurt



[IMG_2679.JPG](#)

Added as Reference

Added on Jul 15, 2026, 3:34 PM CST

Added by kurt kurt



[IMG_2638.jpeg](#)

Added as Reference

Taken on Jul 14, 2026, 12:36 PM CST

Added on Jul 15, 2026, 3:10 PM CST

Added by kurt kurt

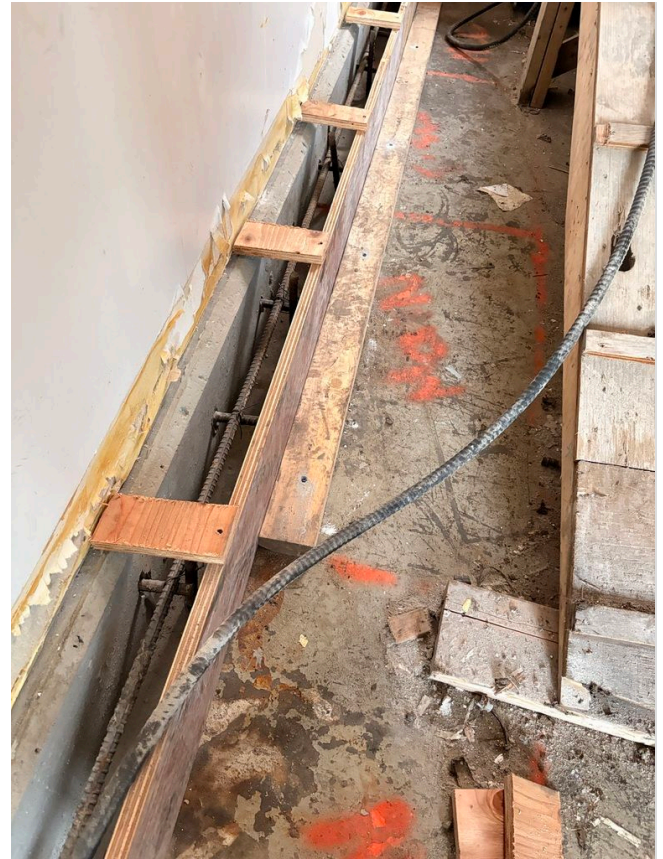
[IMG_2627.jpeg](#)

Added as Reference

Taken on Jul 14, 2026, 11:08 AM CST

Added on Jul 15, 2026, 3:10 PM CST

Added by kurt kurt

[IMG_2732.jpeg](#)

Added as Reference

Taken on Jul 16, 2026, 3:27 PM CST

Added on Jul 17, 2026, 10:11 AM CST

Added by kurt kurt

[IMG_2716.jpeg](#)

Added as Reference

Taken on Jul 16, 2026, 8:36 AM CST

Added on Jul 17, 2026, 10:10 AM CST

Added by kurt kurt

[IMG_2717.jpeg](#)

Added as Reference

Taken on Jul 16, 2026, 8:37 AM CST

Added on Jul 17, 2026, 10:10 AM CST

Added by kurt kurt

[IMG_2722.jpeg](#)

Added as Reference

Taken on Jul 16, 2026, 12:31 PM CST

Added on Jul 17, 2026, 10:11 AM CST

Added by kurt kurt

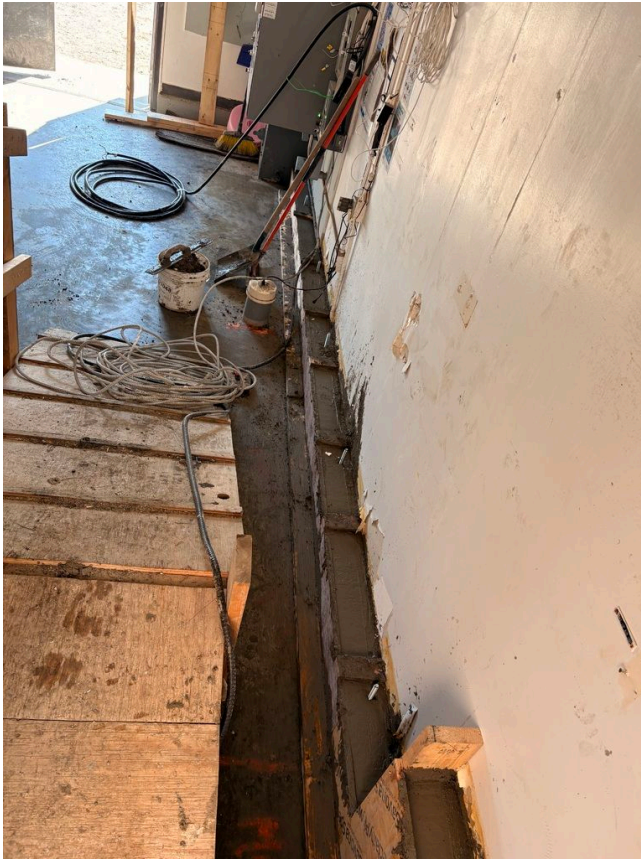
[IMG_2745.jpeg](#)

Added as Reference

Taken on Jul 17, 2026, 10:03 AM CST

Added on Jul 17, 2026, 10:22 AM CST

Added by kurt kurt



[IMG_2743.jpeg](#)

Added as Reference

Taken on Jul 17, 2026, 10:03 AM CST

Added on Jul 17, 2026, 10:22 AM CST

Added by kurt kurt
