

Form detail

#81: Weekly Report # 14 July 20 - July 26, 2026



Forms

Location	
Form date	Jul 20, 2026
Template	Daily Log
Description	Redvers WTP - Weekly Report
Due date	
Created by	kurt kurt
Status	In progress
Last update	Jul 27, 2026, 10:37 AM CST
Last updated by	kurt kurt
Included references	Assets Files Forms Issues Photos File Packages Sheets Submittals RFIs PCOs Schedule Activities

Weather

Rain: 0.02 inches

 Weather [View Sources](#)

7:00 AM

Windy



Temperature: 64°F

Wind: → 16mph

Humidity: 81%

12:00 PM

Windy



Temperature: 72°F

Wind: ↘ 19mph

Humidity: 71%

4:00 PM

Windy



Temperature: 72°F

Wind: ↘ 21mph

Humidity: 70%

Updated Jul 23, 2026 at 7:18 AM

1. Companies On-Site & Manpower

Company	Discipline	Role	# Workers	# Regular hours	# OT hours	Work performed
-	CCR Construction	-	3	-	-	- demolition of curbs for new entrances - built walkway into the overhead door - fill reservoir for hydro static test
-	HB Foundations	-	5	-	-	- patch and plug holes in reservoir - site clean up - demobilize materials
-	TNA Construction	-	5	-	-	- Framing walls - Installed roof sheathing - Installed roof trusses
Totals:			13	0	0	

2. Materials & Shipping

Material	Quantity	Unit	Comment
----------	----------	------	---------

3. Equipment

Equipment	Quantity	Hours used	Comment
-----------	----------	------------	---------

4. Important Conversations

- 4.1 Document all important information / discussions / dates.
Look ahead for the week of July 27 - August 2, 2026

CCR

- Install footing base (weather permitting)
- Hydrostatic testing reservoir
- Demolition of existing curbs
- Miscellaneous tasks

T&A Construction

- Frame walls on ground
- Fly in new walls over existing building
- Fly in new roof over existing building
- Sheet the existing building roof

Elite Excavating

- Backfill around reservoir

Photos (13)[IMG_2758.jpeg](#)**Added as** Reference**Taken on** Jul 20, 2026, 12:59 PM CST**Added on** Jul 23, 2026, 7:21 AM CST**Added by** kurt kurt[IMG_2765.jpeg](#)**Added as** Reference**Taken on** Jul 20, 2026, 2:36 PM CST**Added on** Jul 23, 2026, 7:20 AM CST**Added by** kurt kurt

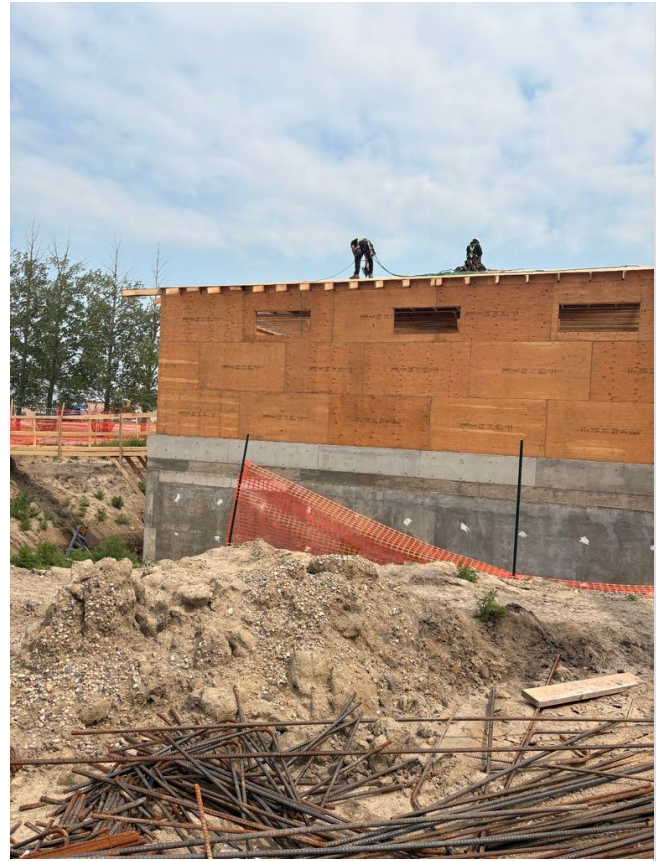
[IMG_2759.jpeg](#)

Added as Reference

Taken on Jul 20, 2026, 12:59 PM CST

Added on Jul 23, 2026, 7:20 AM CST

Added by kurt kurt

[IMG_2757.jpeg](#)

Added as Reference

Taken on Jul 20, 2026, 12:57 PM CST

Added on Jul 23, 2026, 7:20 AM CST

Added by kurt kurt

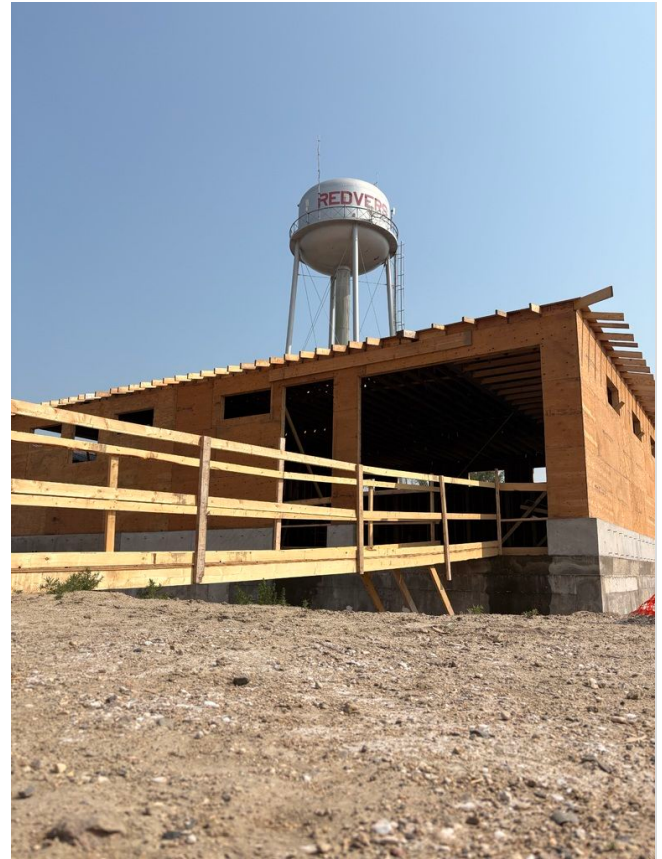
[IMG_2764.jpeg](#)

Added as Reference

Taken on Jul 20, 2026, 2:36 PM CST

Added on Jul 23, 2026, 7:20 AM CST

Added by kurt kurt

[IMG_2849.jpeg](#)

Added as Reference

Taken on Jul 22, 2026, 3:30 PM CST

Added on Jul 22, 2026, 3:46 PM CST

Added by kurt kurt

[IMG_2769.jpeg](#)

Added as Reference

Taken on Jul 20, 2026, 2:57 PM CST

Added on Jul 23, 2026, 7:20 AM CST

Added by kurt kurt

[IMG_2760.jpeg](#)

Added as Reference

Taken on Jul 20, 2026, 12:59 PM CST

Added on Jul 23, 2026, 7:20 AM CST

Added by kurt kurt



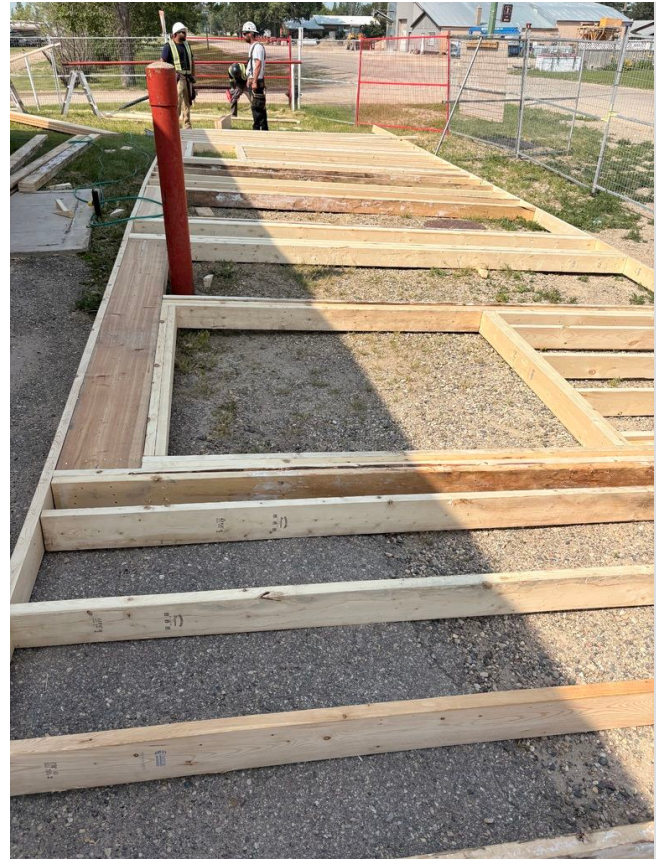
[IMG_2843.jpeg](#)

Added as Reference

Taken on Jul 22, 2026, 2:35 PM CST

Added on Jul 22, 2026, 3:46 PM CST

Added by kurt kurt



[IMG_2851.jpeg](#)

Added as Reference

Taken on Jul 22, 2026, 3:34 PM CST

Added on Jul 22, 2026, 3:46 PM CST

Added by kurt kurt

[IMG_2845.jpeg](#)

Added as Reference

Taken on Jul 22, 2026, 2:35 PM CST

Added on Jul 22, 2026, 3:46 PM CST

Added by kurt kurt

[IMG_2820.jpeg](#)

Added as Reference

Taken on Jul 21, 2026, 3:27 PM CST

Added on Jul 22, 2026, 2:52 PM CST

Added by kurt kurt



[IMG_2815.jpeg](#)

Added as Reference

Taken on Jul 21, 2026, 9:58 AM CST

Added on Jul 22, 2026, 2:52 PM CST

Added by kurt kurt
