

Form detail

#89: Weekly Report # 15 July 27, 2026 - August 2, 2026



Forms

Location	
Form date	Jul 28, 2026
Template	Project Status Report
Description	Weekly Report # 14 July 27 - August 2, 2026
Due date	
Created by	kurt kurt
Status	In progress
Last update	Aug 4, 2026, 11:40 AM CST
Last updated by	kurt kurt
Included references	Assets Files Forms Issues Photos File Packages Sheets Submittals RFIs PCOs Schedule Activities

1. Monday

- 1.1 Date
July 27, 2026
- 1.2 Work Completed
Tasks

Photos (4)



[IMG_2916.jpeg](#)

Added as Reference

Taken on Jul 27, 2026, 3:03 PM CST

Added on Jul 29, 2026, 7:41 AM CST

Added by kurt kurt



[IMG_2912.jpeg](#)

Added as Reference

Taken on Jul 27, 2026, 1:52 PM CST

Added on Jul 29, 2026, 7:41 AM CST

Added by kurt kurt

[IMG_5090.jpeg](#)

Added as Reference

Taken on Jul 23, 2026, 10:01 AM CST

Added on Jul 27, 2026, 9:01 AM CST

Added by Jordan Gent

[IMG_2936.jpeg](#)

Added as Reference

Taken on Jul 28, 2026, 6:13 AM CST

Added on Jul 29, 2026, 7:44 AM CST

Added by kurt kurt



CCR

- Prepped building for removal of walls and roof

TNA Construction

- Frame walls
- Site clean up
- bracing trusses

Elite Excavating

- Brought equipment to site

2. Tuesday

2.1 Date
July 28, 2026

2.2 Work Completed
Tasks

Photos (6)



[IMG_2981.jpeg](#)

Added as Reference

Taken on Jul 28, 2026, 3:07 PM CST

Added on Jul 29, 2026, 7:47 AM CST

Added by kurt kurt



[IMG_2980.jpeg](#)

Added as Reference

Taken on Jul 28, 2026, 2:00 PM CST

Added on Jul 29, 2026, 7:47 AM CST

Added by kurt kurt

[IMG_2971.jpeg](#)

Added as Reference

Taken on Jul 28, 2026, 12:44 PM CST

Added on Jul 29, 2026, 7:46 AM CST

Added by kurt kurt

[IMG_2957.jpeg](#)

Added as Reference

Taken on Jul 28, 2026, 10:45 AM CST

Added on Jul 29, 2026, 7:45 AM CST

Added by kurt kurt



[IMG_2953.jpeg](#)

Added as Reference

Taken on Jul 28, 2026, 10:25 AM CST

Added on Jul 29, 2026, 7:44 AM CST

Added by kurt kurt



CCR

- Demolition of existing building
- Fix electrical pipe that broke
- Site clean up

TNA

- Frame walls
- Fly in walls
- Fly in roof
- Sheet the roof

HB Foundations

- Patch tie holes that are leaking

Flying G Crane

- Fly off old roof
- Fly out old walls
- Fly in new walls



[IMG_2916.jpeg](#)

Added as Reference

Taken on Jul 27, 2026, 3:03 PM CST

Added on Jul 29, 2026, 7:41 AM CST

Added by kurt kurt

- Fly in new roof
- Elite Excavation
- Installing weeping tile
- Monster Hydrovac
- Hydrovac out for weeping tile install

3. Wednesday

- 3.1

Date

July 29, 2026
- 3.2

Work Completed

Tasks

Photos (4)

[IMG_3002.jpeg](#)**Added as** Reference**Taken on** Jul 29, 2026, 2:04 PM CST**Added on** Aug 4, 2026, 11:13 AM CST**Added by** kurt kurt[IMG_3005.jpeg](#)**Added as** Reference**Taken on** Jul 29, 2026, 3:04 PM CST**Added on** Aug 4, 2026, 11:13 AM CST**Added by** kurt kurt




[IMG_3008.jpeg](#)

Added as Reference

Taken on Jul 29, 2026, 3:18 PM CST

Added on Aug 4, 2026, 11:13 AM CST

Added by kurt kurt

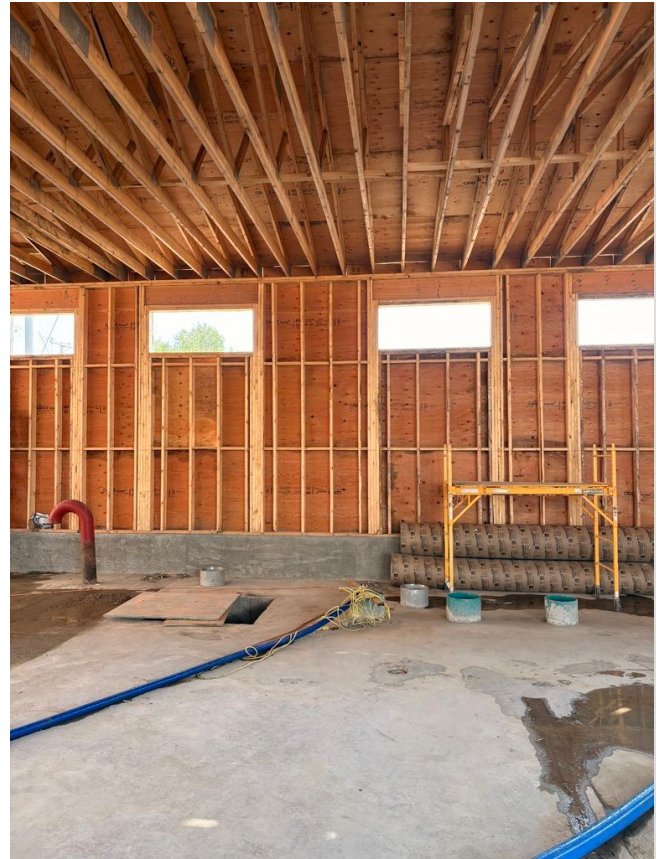

[IMG_3009.jpeg](#)

Added as Reference

Taken on Jul 29, 2026, 3:18 PM CST

Added on Aug 4, 2026, 11:13 AM CST

Added by kurt kurt



CCR Construction

- covering windows in the building
- pumping out reservoir
- fixing piping
- demolition of interior wall

HB Foundations

- Patching the reservoir tie holes that were leaking

TNA Construction

- Framing the roof over existing building

Tuff Exteriors

- Installing membrane on roof
- Rolling out panels for roof

Elite Excavating

- Pick up equipment

BCL Engineering

- Inspection for hydrostatic test

4. Thursday

4.1 Date
July 30, 2026

4.2 Work Completed
Tasks

Photos (6)



[IMG_3050.jpeg](#)

Added as Reference

Taken on Jul 30, 2026, 9:46 AM CST

Added on Aug 4, 2026, 11:30 AM CST

Added by kurt kurt



[IMG_3051.jpeg](#)

Added as Reference

Taken on Jul 30, 2026, 9:49 AM CST

Added on Aug 4, 2026, 11:30 AM CST

Added by kurt kurt




[IMG_3053.jpeg](#)

Added as Reference

Taken on Jul 30, 2026, 11:31 AM CST

Added on Aug 4, 2026, 11:30 AM CST

Added by kurt kurt

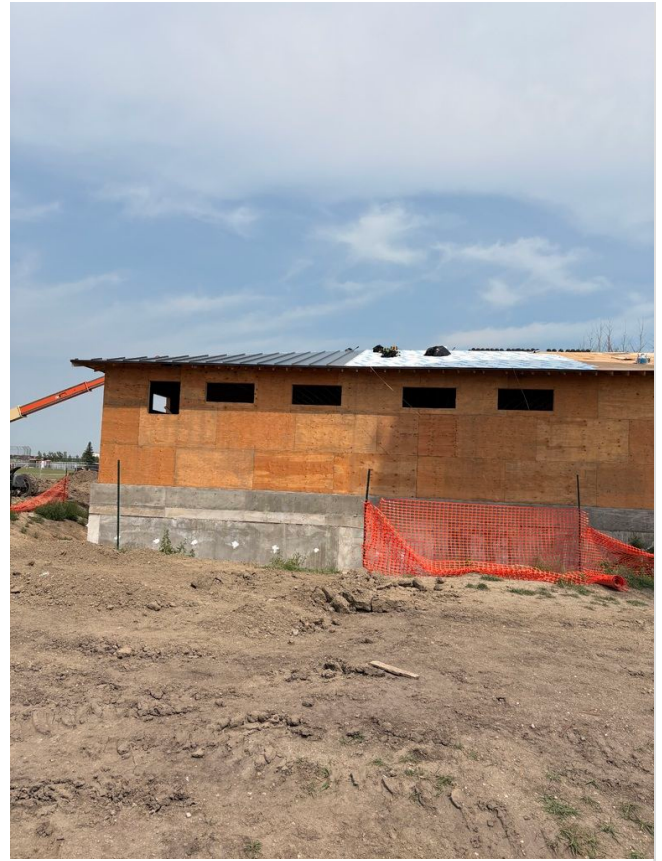

[IMG_3055.jpeg](#)

Added as Reference

Taken on Jul 30, 2026, 11:32 AM CST

Added on Aug 4, 2026, 11:30 AM CST

Added by kurt kurt




[IMG_3060.jpeg](#)

Added as Reference

Taken on Jul 30, 2026, 2:18 PM CST

Added on Aug 4, 2026, 11:30 AM CST

Added by kurt kurt

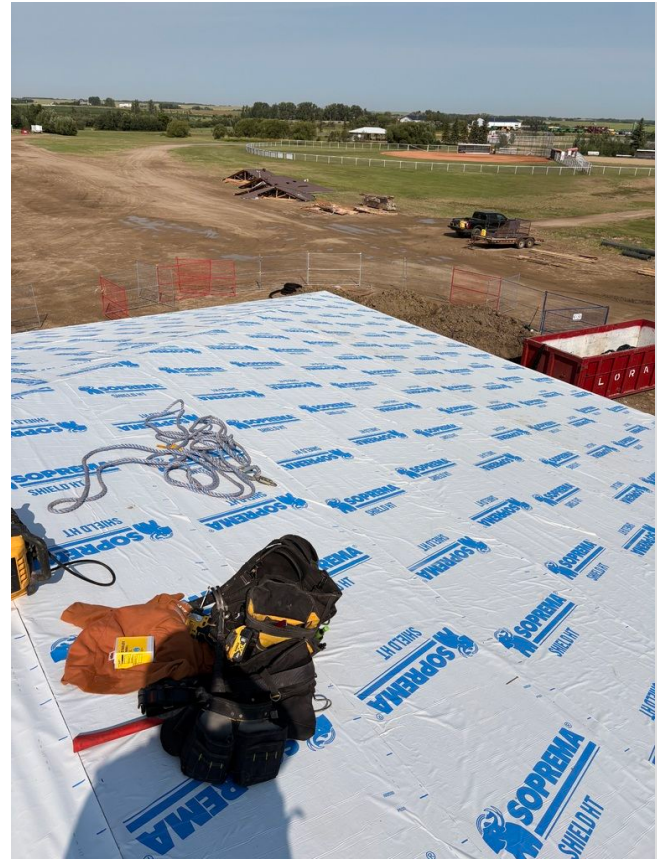

[IMG_3049.jpeg](#)

Added as Reference

Taken on Jul 30, 2026, 9:46 AM CST

Added on Aug 4, 2026, 11:29 AM CST

Added by kurt kurt



CCR Construction

- Draining reservoir for patching
- Site clean up
- Covering openings in the building with tarps
- Building temporary doors

Tuff Exteriors

- Installing roof membrane
- Installing roof panels

TNA Construction

- Sheeting the roof
- Truss blocking

HB Foundations

- Patch leaking holes in the reservoir

5. Friday

5.1 Date

5.2 Work Completed

6. Saturday/Sunday

6.1 Date

6.2 Work Completed

Notes

Look ahead for the week of August 3, 2026 - August 9, 2026
