

Form detail

#101: Project Status Report



Forms

Location

Form date Aug 17, 2026

Template Project Status Report

Description Weekly Report #17 August 10 - August 16, 2026

Due date

Submitted by Jordan Gent

Submitter's company CCR Construction Ltd

Status Closed

Last update Aug 17, 2026, 9:08 AM CST

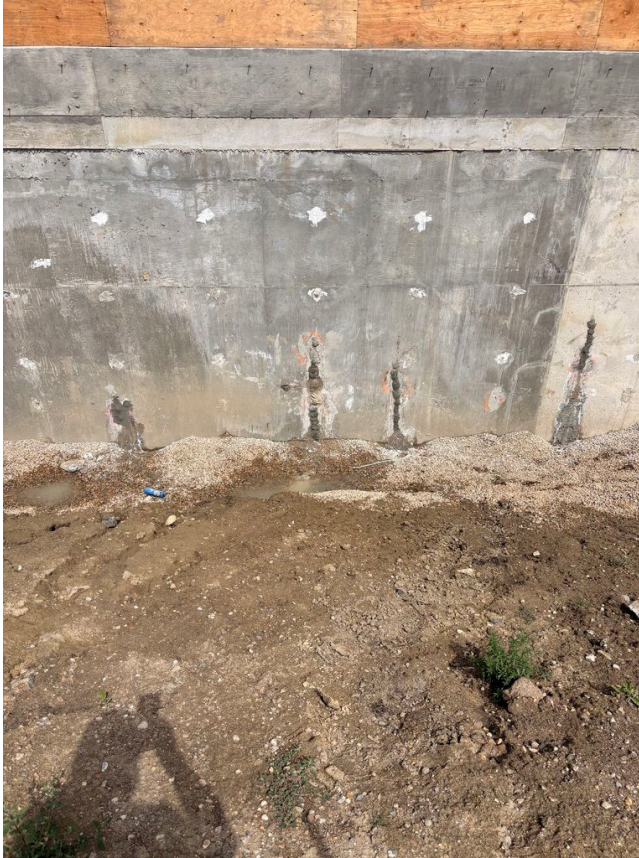
Last updated by Jordan Gent

Included references Assets | Files | Forms | Issues | Photos | File Packages | Sheets | Submittals | RFIs | PCOs | Schedule Activities

1. Monday

1.1 Date
August 10, 2026

1.2 Work Completed
Tasks

Photos (4)

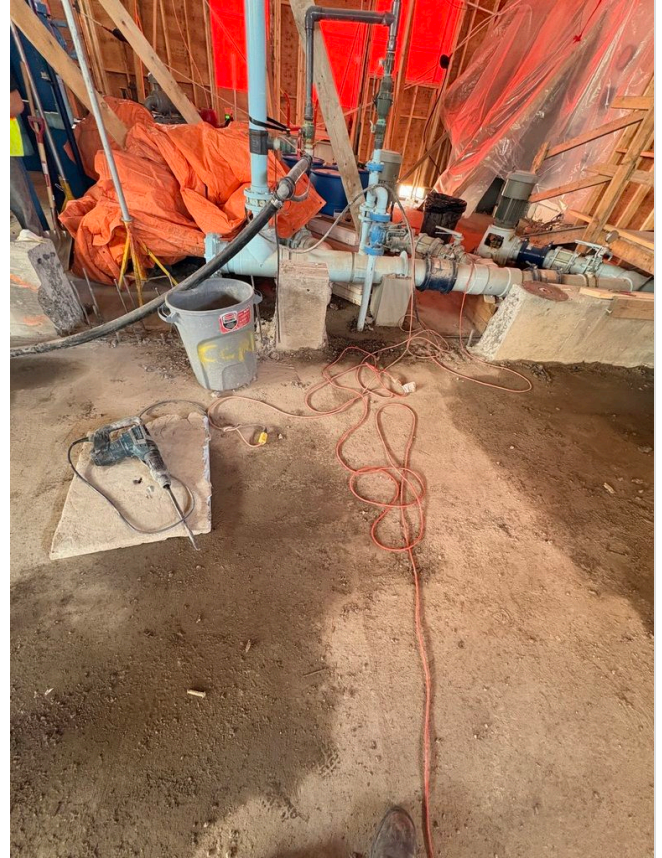
[IMG_3236.jpeg](#)

Added as Reference

Taken on Aug 10, 2026, 12:05 PM CST

Added on Aug 10, 2026, 3:35 PM CST

Added by kurt kurt



[IMG_3225.jpeg](#)

Added as Reference

Taken on Aug 7, 2026, 12:41 PM CST

Added on Aug 10, 2026, 10:57 AM CST

Added by kurt kurt

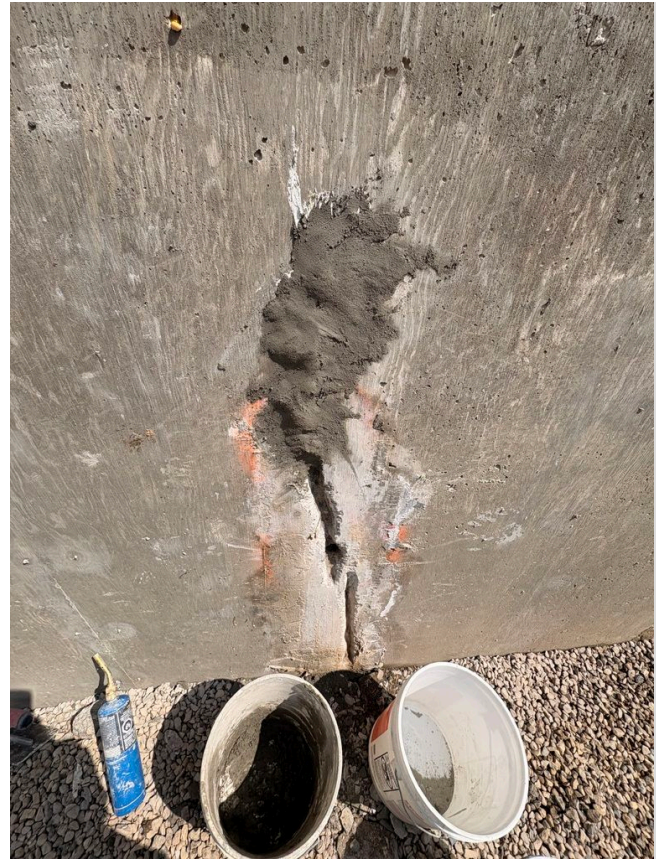
[IMG_3237.jpeg](#)

Added as Reference

Taken on Aug 10, 2026, 12:05 PM CST

Added on Aug 10, 2026, 3:35 PM CST

Added by kurt kurt

[IMG_3246.jpeg](#)

Added as Reference

Taken on Aug 10, 2026, 2:06 PM CST

Added on Aug 10, 2026, 3:35 PM CST

Added by kurt kurt



CCR Construction

- Patch the leaks in the reservoir
- Jack hammer curbs

2. Tuesday

2.1 Date
August 11, 2026

2.2 Work Completed
Tasks



CCR Construction

- Patch the leaks in the reservoir
- Jack hammer curbs

3. Wednesday

3.1 Date
August 12, 2026

3.2 Work Completed
Tasks



CCR Construction
- Patch the leaks in the reservoir

4. Thursday

4.1 Date
August 13, 2026

4.2 Work Completed
Tasks

Photos (4)



[IMG_7959.jpeg](#)

Added as Reference

Taken on Aug 13, 2026, 11:53 AM CST

Added on Aug 13, 2026, 6:37 PM CST

Added by Garry Kabera



[IMG_7965.jpeg](#)

Added as Reference

Taken on Aug 13, 2026, 12:15 PM CST

Added on Aug 13, 2026, 6:37 PM CST

Added by Garry Kabera



[IMG_7958.jpeg](#)

Added as Reference

Taken on Aug 13, 2026, 11:53 AM CST

Added on Aug 13, 2026, 6:37 PM CST

Added by Garry Kabera



[IMG_7966.jpeg](#)

Added as Reference

Taken on Aug 13, 2026, 12:15 PM CST

Added on Aug 13, 2026, 6:37 PM CST

Added by Garry Kabera



CCR Construction

- Patch the leaks in the reservoir to prep for damp proofing
- Jack hammer curbs

Northern Tar

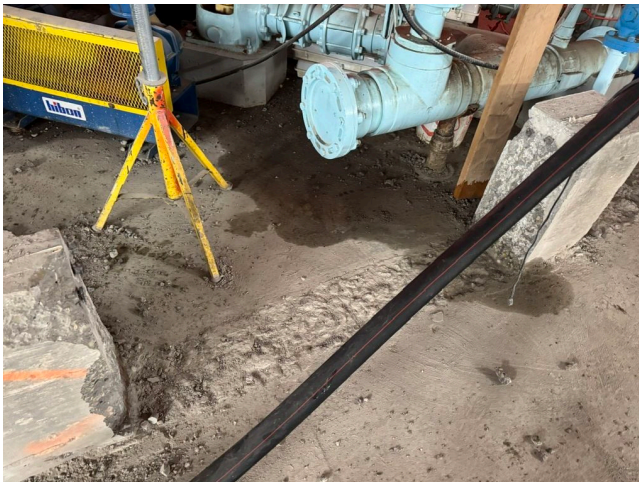
- Apply damp proofing to reservoir

5. Friday

5.1 Date
August 15, 2026

5.2 Work Completed
Tasks

Photos (6)

[IMG_7994.jpeg](#)**Added as Reference****Taken on** Aug 14, 2026, 1:26 PM CST**Added on** Aug 14, 2026, 3:44 PM CST**Added by** Garry Kabera[IMG_7996.jpeg](#)**Added as Reference****Taken on** Aug 14, 2026, 1:26 PM CST**Added on** Aug 14, 2026, 3:44 PM CST**Added by** Garry Kabera[IMG_7995.jpeg](#)**Added as Reference****Taken on** Aug 14, 2026, 1:26 PM CST**Added on** Aug 14, 2026, 3:44 PM CST**Added by** Garry Kabera[IMG_7992.jpeg](#)**Added as Reference****Taken on** Aug 14, 2026, 9:05 AM CST**Added on** Aug 14, 2026, 3:45 PM CST**Added by** Garry Kabera



[IMG_8002.jpeg](#)

Added as Reference

Taken on Aug 14, 2026, 1:28 PM CST

Added on Aug 14, 2026, 3:45 PM CST

Added by Garry Kabera



CCR Construction

- Jack hammer curbs

BCL

- Site Inspection including inspection of the damp proofing



[IMG_8001.jpeg](#)

Added as Reference

Taken on Aug 14, 2026, 1:28 PM CST

Added on Aug 14, 2026, 3:45 PM CST

Added by Garry Kabera

6. Saturday/Sunday

6.1 Date
August 15-16

6.2 Work Completed
N/A

Notes

Look ahead for the week of August 17 - August 21, 2026

Elite Trenching
- Backfilling

CCR Construction
- installing rigid insulation
- finish jack hammering concrete
- create forms and make dowels
- demo roof
